

PERMIT

SEWAGE DISPOSAL SYSTEM

DEPARTMENT OF HEALTH AND MENTAL HYGIENE

04-355849

HOWARD COUNTY HEALTH DEPARTMENT

BUREAU OF ENVIRONMENTAL HEALTH

~~XXX-XXX-XXXX~~

410-313-2640

P 5/10/21-B

A 34853

DISTRICT 4th

DATE 5-4-98

DATE SYSTEM APPROVED 5/21/98

INSPECTOR AL

Jack Fyock Septice Service

IS PERMITTED TO INSTALL X ALTER

ADDRESS 13775 Triadelphia Rd, Glenelg, MD 21737

PHONE 410-988-9270

SUBDIVISION Sharp Farms

LOT 34

ROAD 3951 Sharp Road

PROPERTY OWNER Bryan & Lisa Thrush

ADDRESS

SEPTIC TANK CAPACITY 1250 GALLONS

NUMBER OF BEDROOMS 4

240 SQUARE FEET PER BEDROOM

LINEAR FEET OF TRENCH REQUIRED 320

TRENCHES - Trench to be 3 feet wide. Inlet 4½ feet below original grade. Bottom maximum depth 6½ feet below original grade. Effective area begins at 4½ feet below original grade. 2 feet of stone below distribution pipe.

LOCATION - Place the distribution box 175 feet from the North (443') lot line and 10 feet from the East (576') lot line. Run trenches along contour toward the East (576') lot line.

NOTES - No trench to exceed 100 feet in length. Provide 6" - 8" diameter cleanout and cap to grade or above on septic tank. OK 2/25/98

PLANS APPROVED BY C. Williams

REVISED DATE 01/26/98

COVER NO WORK UNTIL INSPECTED AND APPROVED

NEITHER THE HOWARD COUNTY COUNCIL NOR THE HEALTH DEPARTMENT IS RESPONSIBLE FOR THE SUCCESSFUL OPERATION OF ANY SYSTEM

NOTE: CLEANOUT REQUIRED EVERY 70 FEET OF SEWER LINE AND/OR AT 90° SWEEPS IN LINES FROM HOUSE TO DRAIN FIELDS, 90° ELBOWS NOT ACCEPTABLE.

NOTE: ALL PARTS OF SEPTIC SYSTEMS (I.E. TANK, DISTRIBUTION BOX TRENCHES) TO BE 100 FEET FROM WELL (UNLESS OTHERWISE SPECIFICALLY AUTHORIZED)

NOTE: IF DEEP TRENCH(ES) ARE USED CALL FOR INSPECTION BEFORE AND AFTER PLACING GRAVEL IN TRENCH(ES)

NOTE: NO DRY WELL SHALL EXCEED 15 FOOT IN DIAMETER NO ABSORPTION TRENCH TO EXCEED 100 FEET IN LENGTH


NOTE: ALL PIPE FROM HOUSE TO SEPTIC TANK MUST BE CAST IRON OR SCHEDULE 35/40 PVC OR ABS

PERMIT VOID AFTER TWO YEARS

NOTE: INSTALL STAND PIPE ON SEPTIC TANK AND DRY WELL STAND PIPES MUST BE 6 INCHES IN DIAMETER CAST IRON. CONCRETE OR TERRA COTTA OR PVA OR ABS ACCEPTED. IF TOP OF SEPTIC TANK IS DEEPER THAN 3 FEET. MANHOLE TO GRADE REQUIRED.

NOTE: DISTRIBUTION BOXES MUST HAVE BAFFLES

***INSTALLER IS RESPONSIBLE FOR OBTAINING FINAL APPROVAL ON THIS PERMIT**

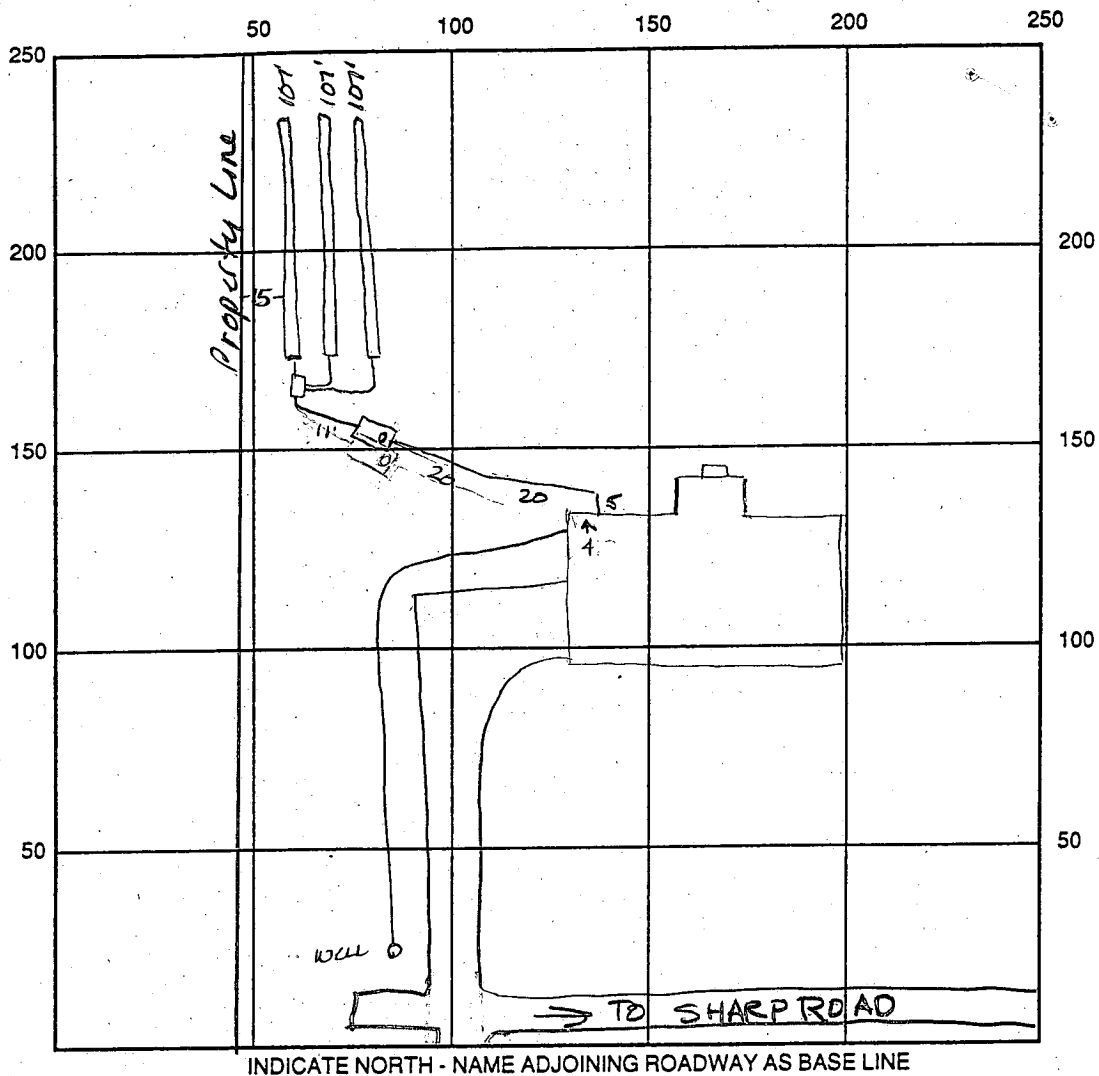

SEPTIC TANK LEVEL 1500.9a1 CLEANOUTS OK

DISTRIBUTION BOX LEVEL OK baffle is in

DRAIN FIELD/TITLE DEPTH 6.5' FT. TRENCH WIDTH 3.0 FT. INLET DEPTH 4.0 FT.

EFFECTIVE GRAVEL DEPTH 2.0 FT. TOTAL LENGTH 321 FT.

NUMBER OF TRENCHES 3 ONE SIDEWALL/BOTTOM AREA 963 SQ. FT.

DRYWALL INSIDE DIAMETER — FT. EFFECTIVE DEPTH BELOW INLET 2.0 FT.

ABSORBENT AREA — SQ. FT.

REMARKS: 5/7/98 OK to cover all work - house connection needed

5/21/98 House connection made

DATE SYSTEM APPROVED 5/21/98 INSPECTOR Amy McMillan

November 24, 1997

Craig Williams.

Please review enclosed plat with "proposed" house site.

I will call you Tuesday to discuss.

Thanks for your time.

Sincerely,

Bryan Thrush
301-210-7377

11/24/97

BRYAN - WITH 20' BUFFER HOUSE → SEPTIC,
MORE THAN HALF THE AREA IS LOST.

WET SEASON TESTING WOULD BE NEEDED
FOR FINAL DETERMINATION AND EVEN THEN
IT WOULD BE "PUSHING THE REVIEWER'S JUDGEMENT"
ON IMPACT OF FUTURE FLUCTUATIONS IN WATER TABLE.
THAT'S A BAD RISK!

SURELY THAT'S NOT THE ONLY SUITABLE HOUSE POSITION

PLUS - IF YOU ONLY HAVE MINIMUM SEPARATION BETWEEN
HOUSE & SEPTIC NOW, YOU'VE LOCKED YOURSELF OUT OF
FUTURE DECK - PATIO - POOL IN ANY NORMAL CONFIGURATION.
PICK A SITE AWAY FROM THE SEPTIC, PUMP THE SEWAGE, & ENJOY THE LOT.

(CW)

NOV 24 P 3:06

APPLICATION

PERCOLATION TESTING

Previous 34853
A _____

P _____

HOWARD COUNTY HEALTH DEPARTMENT

BUREAU OF ENVIRONMENTAL HEALTH

3525-H ELLICOTT MILLS DRIVE/ELLICOTT CITY, MARYLAND 21043
TELEPHONE: 313-2640

Reperc requested

by Health Dept. DISTRICT _____

- No fee

DATE _____

TO: THE COUNTY HEALTH OFFICER
ELLICOTT CITY, MARYLAND

I HEREBY APPLY FOR THE NECESSARY TEST PRIOR TO APPLICATION FOR PERMIT TO CONSTRUCT (OR RECONSTRUCT) A SEWAGE DISPOSAL SYSTEM.

PROPERTY OWNER Charles Sharp Bryan + Lisa Thrush

ADDRESS _____ PHONE _____

AGENT OR PROSPECTIVE BUYER Brian Thrush

ADDRESS 4206 TAUNTON DRIVE PHONE (301) 937-1762
BELTSVILLE 20705

PROPERTY LOCATION:

SUBDIVISION Sharp Farms LOT NO. 34

ROAD AND DESCRIPTION 3957 Sharp Road

BLDG. PERMIT SIGNED

AND RETURNED

Serial # B10109312

TAX MAP _____ PARCEL # _____

SIZE OF LOT _____ TYPE BLDG. SFD - 4 Bdrm.
(SINGLE FAMILY DWELLING OR COMMERCIAL)

THE SYSTEM INSTALLED UNDER THIS APPLICATION IS ACCEPTABLE ONLY UNTIL PUBLIC FACILITIES BECOME AVAILABLE. I FULLY UNDERSTAND THE FEE CONNECTED WITH THE FILING OF THIS PERC TEST APPLICATION IS NON-REFUNDABLE UNDER ANY CIRCUMSTANCES. I ALSO AGREE TO COMPLY WITH ALL M.O.S.H.A. REQUIREMENTS IN TESTING THIS LOT.

(SIGNATURE OF APPLICANT)

APPROVED BY _____ FOR _____ DATE _____

DISAPPROVED BY _____ FOR _____ DATE _____

HOLD PENDING FURTHER TESTS _____

REASONS FOR REJECTION OR HOLDING _____

PERCOLATION TEST PLAT/PRELIMINARY PLAT - TITLE OR I.D. # _____ DATE _____

SITE DEVELOPMENT PLAN/FINAL PLAT - TITLE OR I.D. # _____ DATE _____

THIS IS NOT A PERMIT

A34853 REPEAT

NEIGHBORING WELL


COUNTY #

SOIL PROFILE

0'
#1
CLAY
CLAY LOAM 4'
SILT LOAM 6'
MOTTLED 11'
12'

#2
CLAY
SILT LOAM 6'
SATURATED TO 7'
WATER 10'

#3
SIMILAR TO #1 BUT LOWER ON LANDSCAPE AND CLOSER TO NEIGHBORING WELL

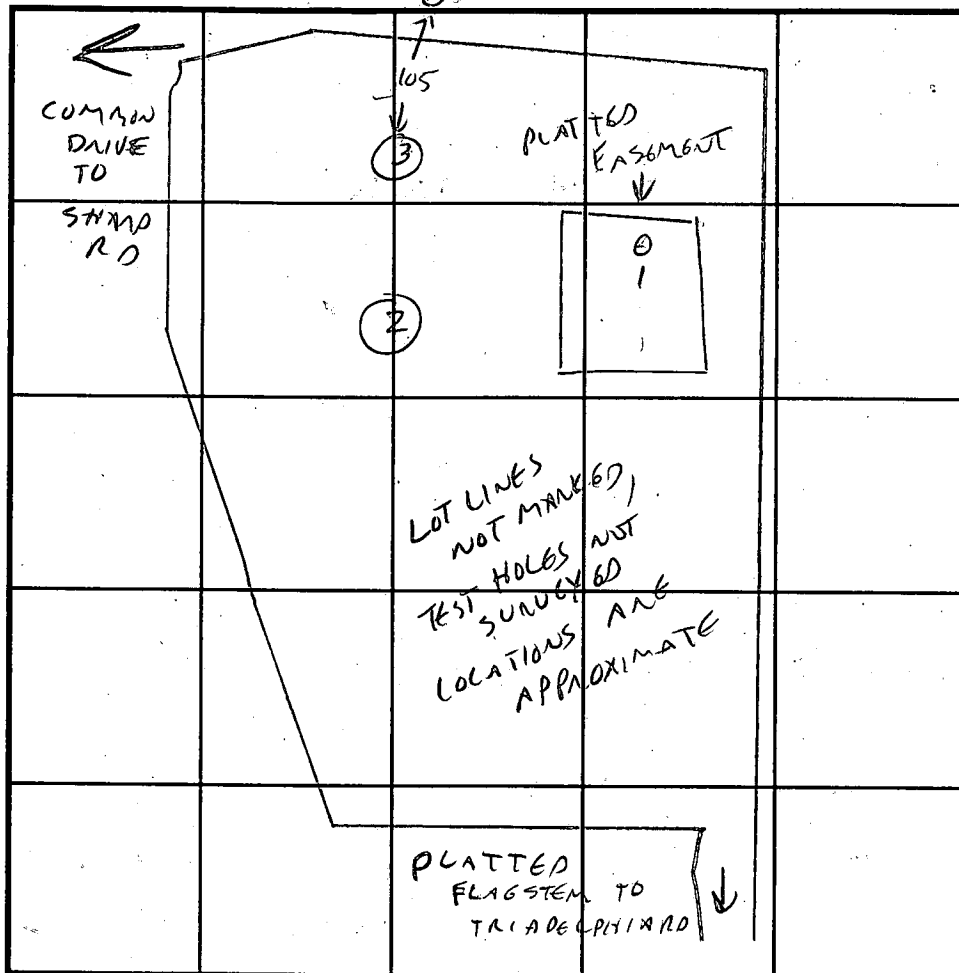

SOIL PROFILE

0'

INDICATE NORTH - NAME ADJOINING ROADWAY AS BASE LINE.

DATE	TEST NO.	DEPTH	PRE-WET		TEST - 1" DROP		TIME	
			START	STOP	START	STOP		
11/3/97	1	6	2:05	2:12	2:12	2:24	12	
		12	VIS OK	LOAM	6-11'			
			NO WATER, MOTTLED AT				11-12'	
	2	VISUAL UNACCEPTABLE						
		CLAY TO 6' WATER AT 10'						
		SOILS SATURATED TO						7'
	3	SIMILAR TO HOLE 1, BUT NOT RECOMMENDED FOR						
		DEEP CLAY, MOTTLED AT 11', LOWER ON LOT 9						
		CLOSER TO NEIGHBORING WELL -						
		TRENCH DESIGN DATA: AVERAGE PERCOLATION TIME						11'

REMARKS CONDITIONS IN HOLE 3 "RIPE" FOR GREATER THAN USUAL CHANGE IN WATER TABLE

TYPE OF SOIL RECOMMENDATIONS

TESTED BY: C. W. R. H. ALSO PRESENT: SHARP, THOUGH, ROBT F. YOCK

TRENCH DESIGN DATA: AVERAGE PERCOLATION TIME 12 MIN TRENCH WIDTH 3

INLET DEPTH 4 MAXIMUM BOTTOM DEPTH 6 SQ. FT./BEDROOM 240

APPLICATION

SEWAGE DISPOSAL TESTING

STATE OF MARYLAND - DEPARTMENT OF HEALTH AND MENTAL HYGIENE

HOWARD COUNTY HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH SERVICES

P. O. BOX 476 ELLICOTT CITY, MARYLAND 21043
TELEPHONE: 992-2330

A 34P53

P _____

DISTRICT 4

DATE Jan 2, 1985

TO: THE COUNTY HEALTH OFFICER
ELLICOTT CITY, MARYLAND

I, HEREBY, APPLY FOR THE NECESSARY TEST IN ORDER TO CONSTRUCT (OR RECONSTRUCT) A SEWAGE DISPOSAL SYSTEM.

PROPERTY OWNER Charles A. Sharp

ADDRESS 3779 Sharp Road Glenwood Md 21738 PHONE 489-4630

PROPERTY LOCATION:

SUBDIVISION ~~A6~~ LOT NO. #9

ROAD AND DESCRIPTION Northwest side Triadelphia Rd, 600' NE of Sharp Rd.

SIZE OF LOT 3 ac TYPE BLDG. Residence
(NUMBER OF BEDROOMS)

THE SYSTEM INSTALLED UNDER THIS APPLICATION IS ACCEPTABLE ONLY UNTIL PUBLIC FACILITIES BECOME AVAILABLE. I FULLY UNDERSTAND THE FEE CONNECTED WITH THE FILING OF THIS PERC TEST APPLICATION IS NON-REFUNDABLE UNDER ANY CIRCUMSTANCES. I ALSO AGREE TO COMPLY WITH ALL M.O.S.H.A. REQUIREMENTS IN TESTING THIS LOT.

Charles A. Sharp
(SIGNATURE OF APPLICANT)

APPROVED BY _____ FOR _____ DATE _____

REJECTED BY _____ FOR _____ DATE _____

HOLD PENDING FURTHER TESTS _____ DATE _____


REASONS FOR REJECTION OR HOLDING _____

THIS IS NOT A PERMIT

LOT 2 m F-8759
LOT 10

①
SOIL PROFILE

BROWN CLAY
BROWN SAND SILT LOAM
WATER

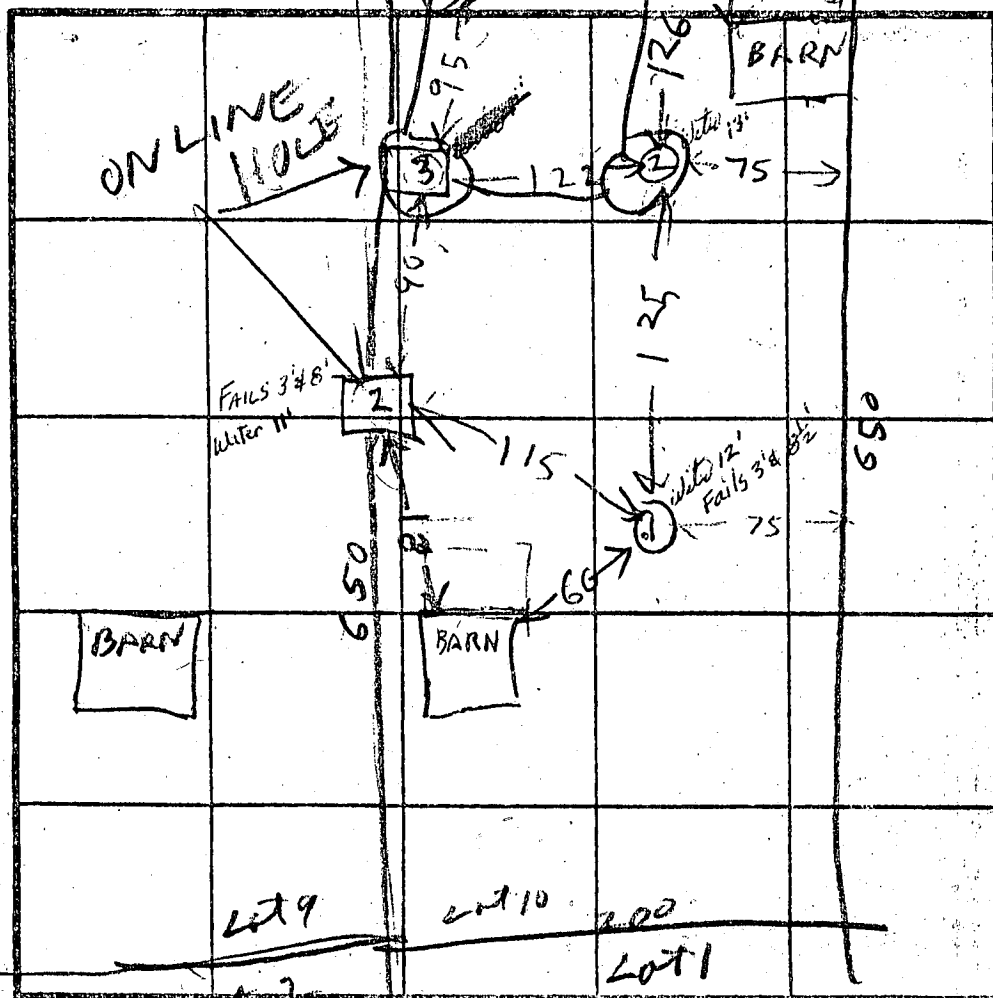

④
BROWN CLAY
BROWN & GRAY SAND LOAM
⑤
CLAY
BROWN SAND SILT LOAM
WATER

BROWN CLAY
BROWN SAND
WATER
B
BROWN CLAY
BROWN SAND SILT LOAM
WATER

INDICATE NORTH - NAME ADJOINING ROADWAY AS BASE LINE.

DATE	TEST NO.	DEPTH	PRE-WET		TEST - 1" DROP		TIME
			START	STOP	START	STOP	
3/1/85	1 S	5 1/2	1135	1144	1144	1214	30
	2 S	13	WATER	12			
	2 S	5 1/2	1144	1158	1158	1236	38
	2 V	14	WATER	13 FT			
	12	13	ON LINE HOLE BETWEEN LOT 9 & 10 See Sheet on 7				
OK	3 S	5 1/2	1208	1209	1209	1211	2
	3 V	12 1/2	LOOK	OK	BELOW 3 FT		
	3 ES	3	143	146	146	156	10
	2 ES	3	145	208	208	230	22
OK	2 M	7.5	200	208	208	218	10
	1 ES	3	212	245	LITTLE PERC		
	1 M	8 1/2	212	245	water 2 33		
	4 S		255	258	258	301	
3/1/85	5 S	4	311	321	321	336	15
	5 V	12	WATER	11 FT			

REMARKS

3 - ON LINE HOLE BETWEEN LOT 9 & LOT 10

TYPE OF SOIL

COLLINS B. PHOENIX & SHARP Owners


TESTED BY


R. HODGES

ALSO PRESENT

C. SHARP

69.050	27	521327.635	797474.812
66.080	28	520683.342	796825.805
89.731	29	520893.894	797260.842
10.015	30	521437.742	796902.272
86.643	31	521239.177	797095.606
270.627	33	521007.650	798009.303

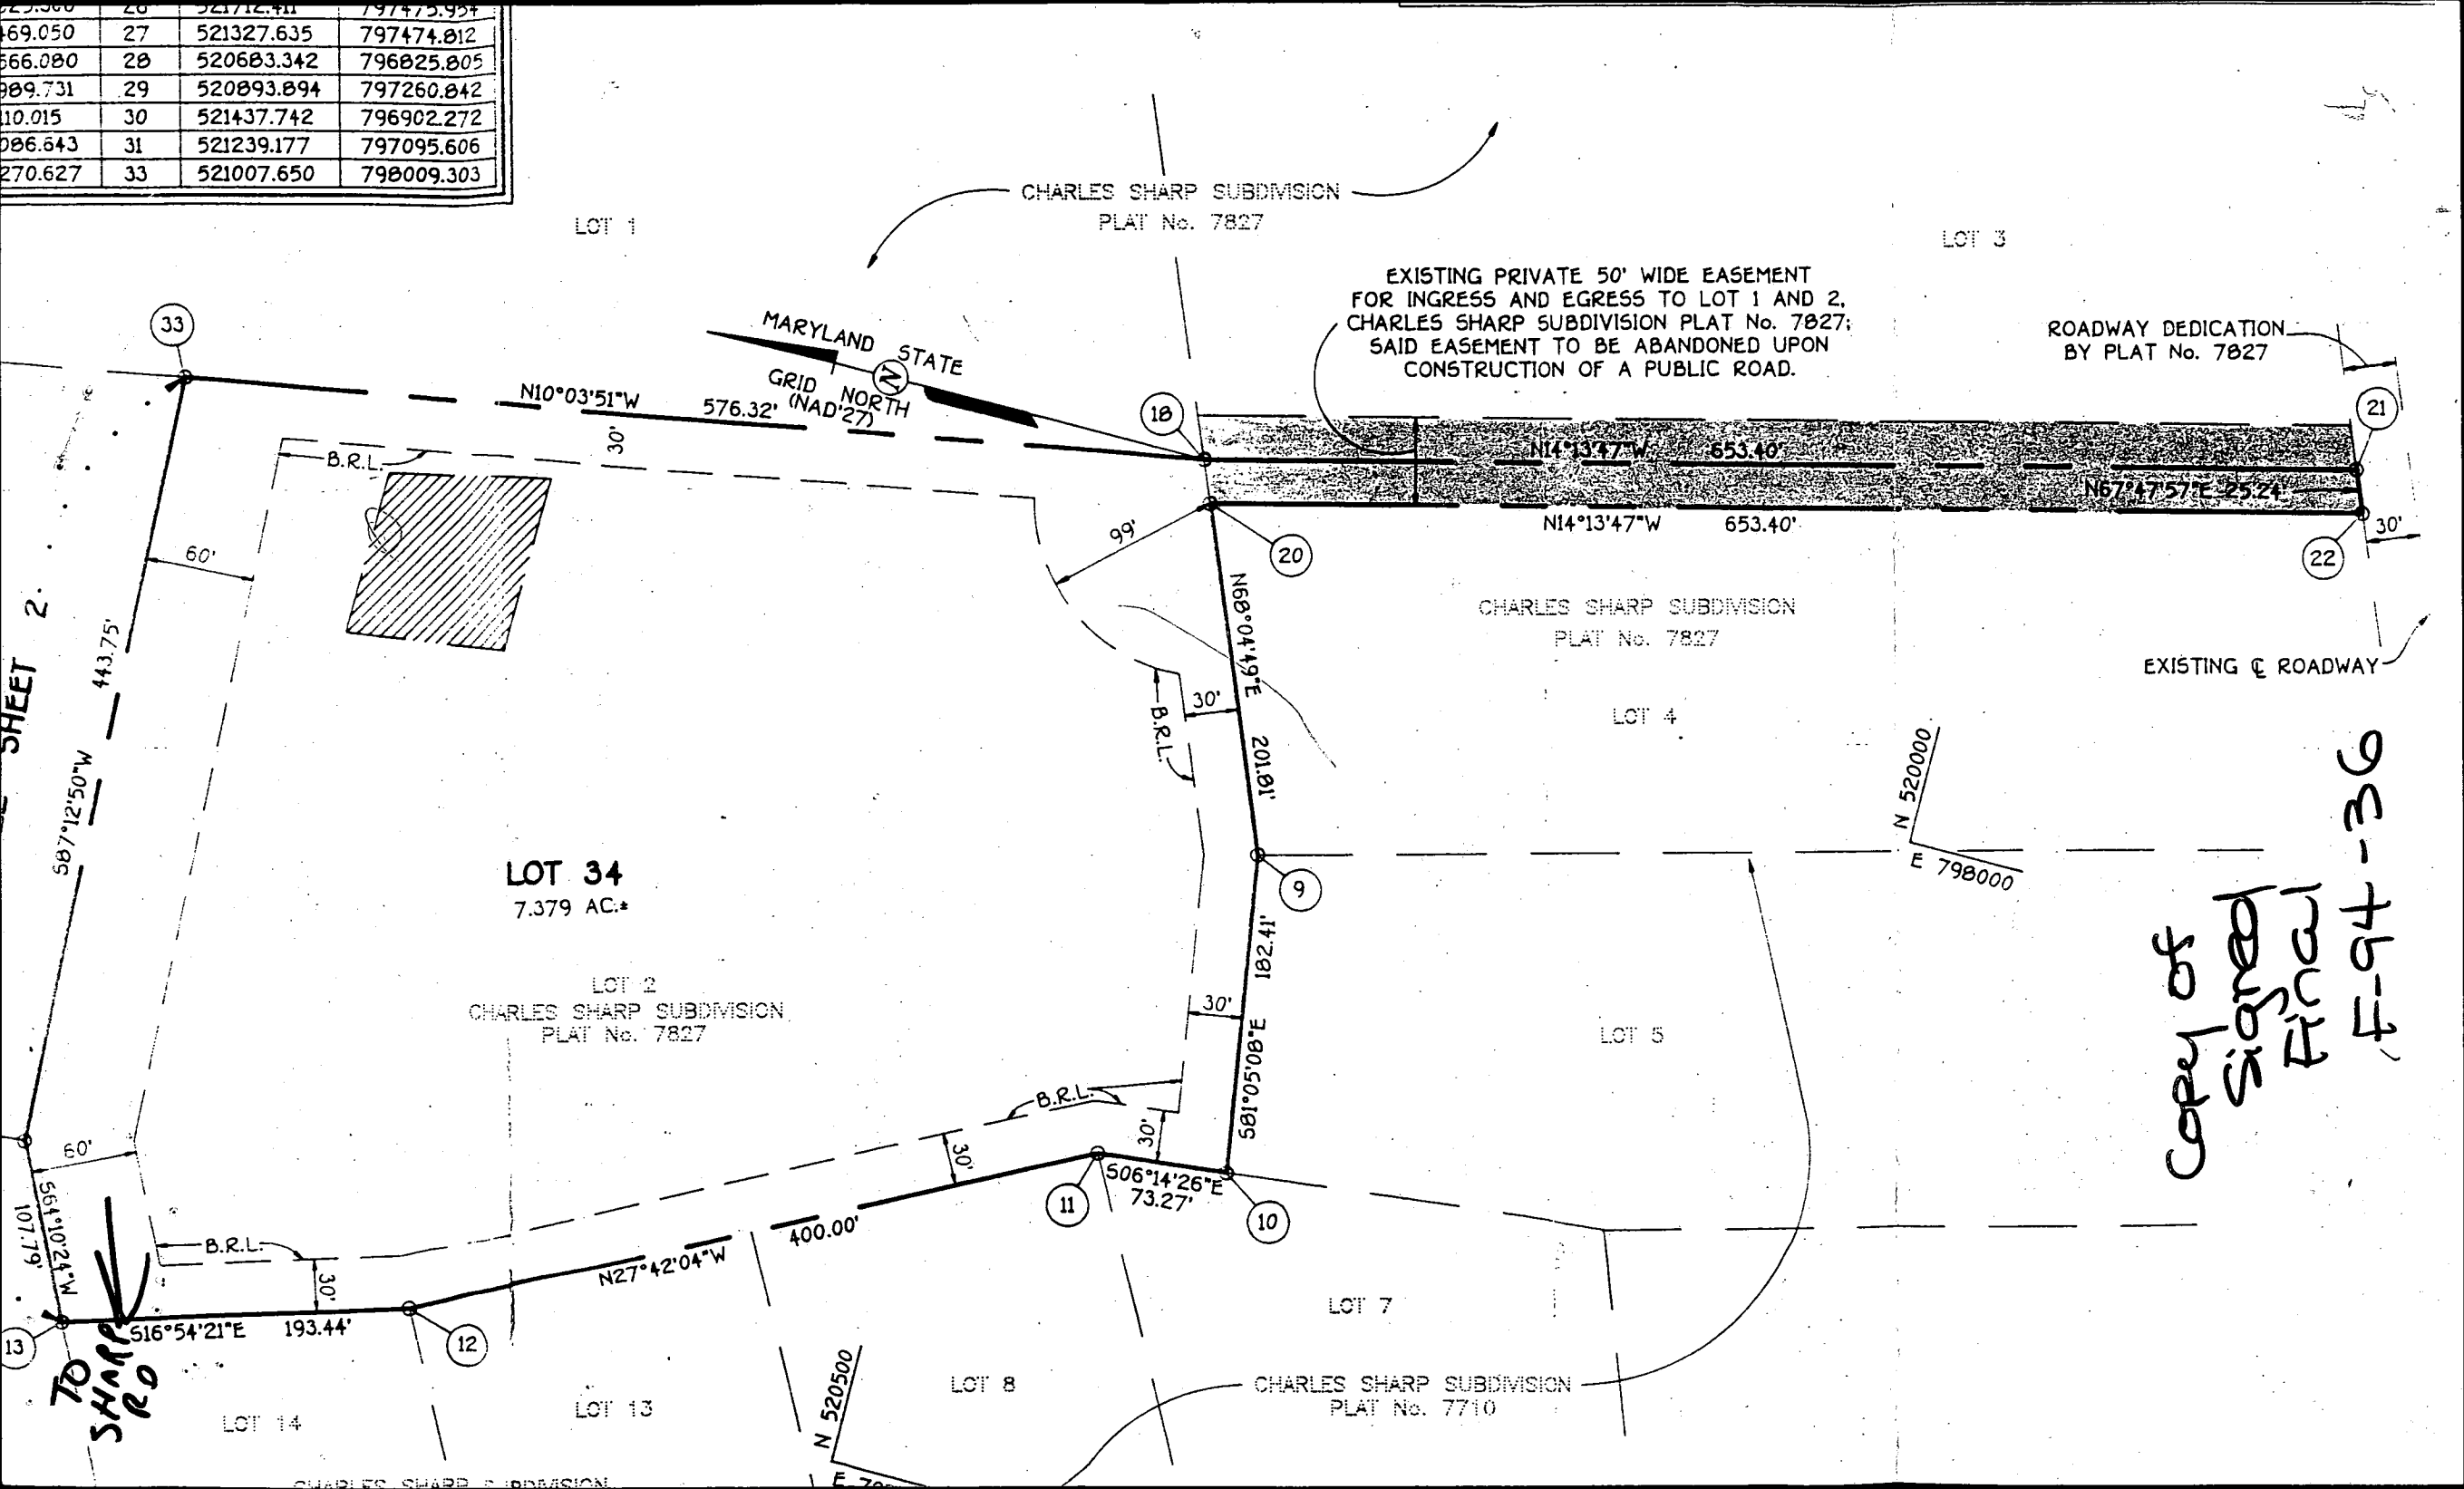

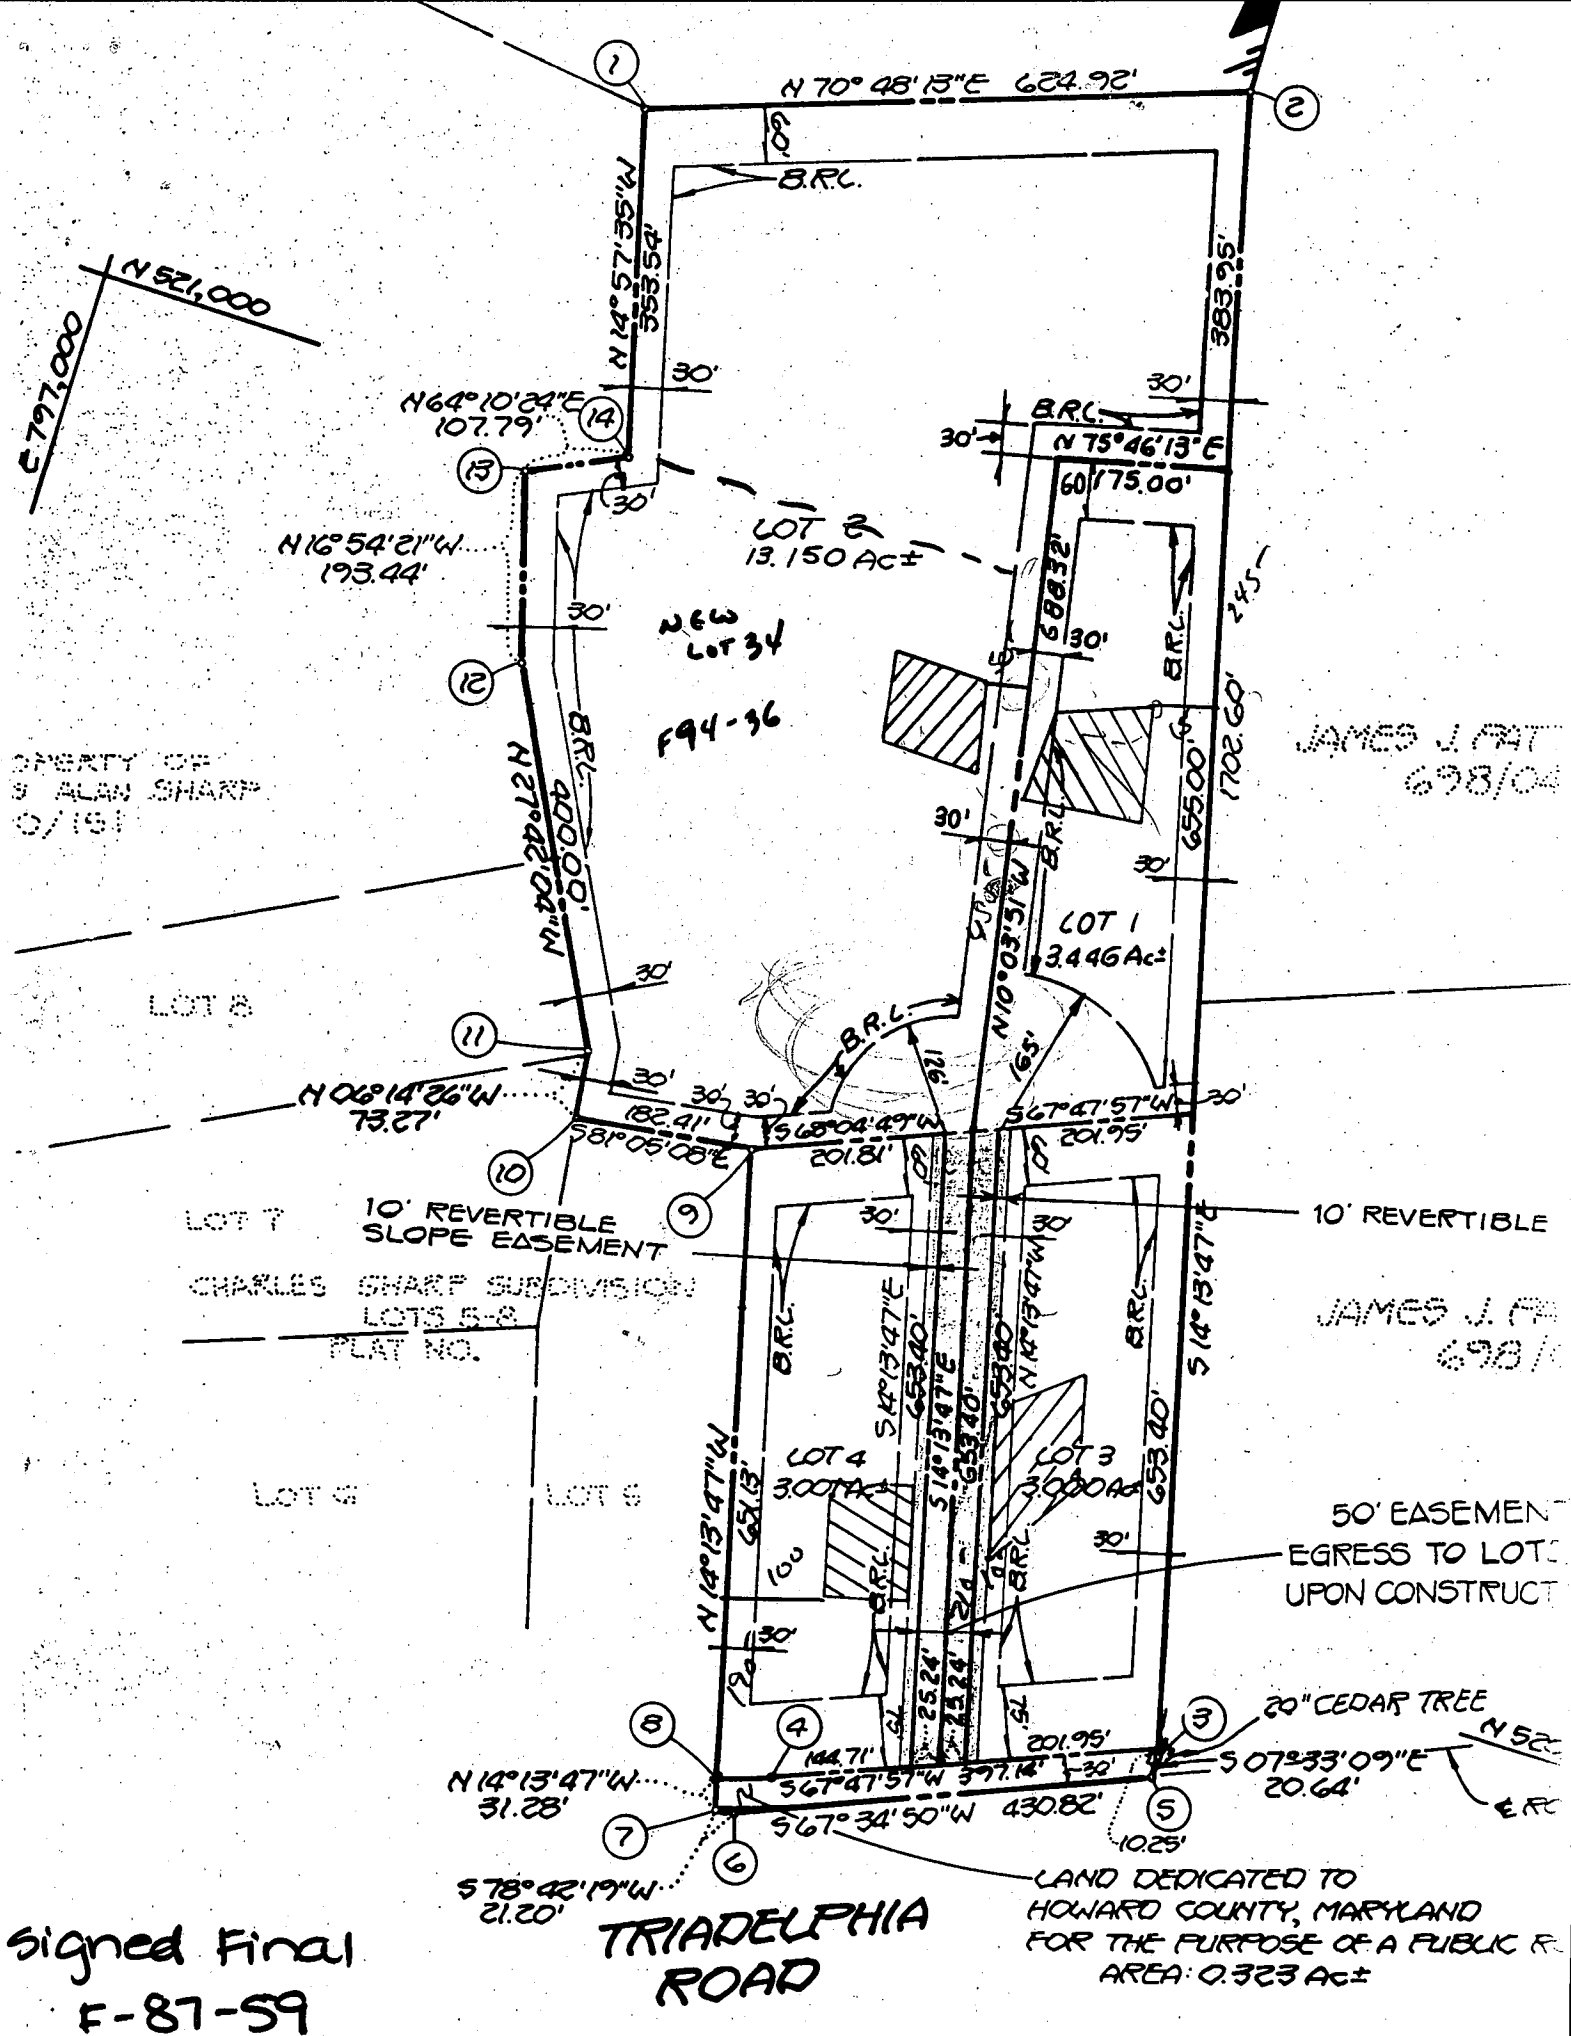

4-23-98
10:00

APPLICATION

PERCOLATION TESTING

A 59940

P _____

HOWARD COUNTY HEALTH DEPARTMENT

BUREAU OF ENVIRONMENTAL HEALTH

3525-H ELLICOTT MILLS DRIVE/ELLICOTT CITY, MARYLAND 21043
TELEPHONE: 313-2640

DISTRICT _____

DATE 4/14/98

TO: THE COUNTY HEALTH OFFICER
ELLICOTT CITY, MARYLAND

4/14/98
*Preview OK -
Adjustment to
recorded SDA.
AM*

I HEREBY APPLY FOR THE NECESSARY TEST PRIOR TO APPLICATION FOR PERMIT TO CONSTRUCT (OR RECONSTRUCT) A SEWAGE DISPOSAL SYSTEM.

PROPERTY OWNER Bryan + Lisa Thrush

ADDRESS 11616 Clocktower Lane, Laurel MD 20708 PHONE 301-210-7377

AGENT OR PROSPECTIVE BUYER _____

ADDRESS _____ PHONE _____

PROPERTY LOCATION:

SUBDIVISION Sharp Farms LOT NO. 34

ROAD AND DESCRIPTION Sharp Rd

TAX MAP _____ PARCEL # _____

SIZE OF LOT _____ TYPE BLDG. _____
(SINGLE FAMILY DWELLING OR COMMERCIAL)

THE SYSTEM INSTALLED UNDER THIS APPLICATION IS ACCEPTABLE ONLY UNTIL PUBLIC FACILITIES BECOME AVAILABLE. I FULLY UNDERSTAND THE FEE CONNECTED WITH THE FILING OF THIS PERC TEST APPLICATION IS NON-REFUNDABLE UNDER ANY CIRCUMSTANCES. I ALSO AGREE TO COMPLY WITH ALL M.O.S.H.A. REQUIREMENTS IN TESTING THIS LOT.

(SIGNATURE OF APPLICANT)

APPROVED BY _____ FOR _____ DATE _____

DISAPPROVED BY _____ FOR _____ DATE _____

HOLD PENDING FURTHER TESTS _____

REASONS FOR REJECTION OR HOLDING _____

PERCOLATION TEST PLAT/PRELIMINARY PLAT - TITLE OR I.D. # _____ DATE _____

SITE DEVELOPMENT PLAN/FINAL PLAT - TITLE OR I.D. # _____ DATE _____

THIS IS NOT A PERMIT

SQ. FT./BEDROOM

water coming in @ 5.0

C1 09498

SEQUENCE NO.
(MDE USE ONLY)STATE OF MARYLAND
WELL COMPLETION REPORT
FILL IN THIS FORM COMPLETELY
PLEASE PRINT OR TYPETHIS REPORT MUST BE SUBMITTED WITHIN
45 DAYS AFTER WELL IS COMPLETED.COUNTY
NUMBER A34853

ST/CO USE ONLY

DATE RECEIVED

MM/DD/YY
11/15/97

DATE WELL COMPLETED

MM/DD/YY
11/25/97

Depth of Well

22 160 26
(TO NEAREST FOOT)PERMIT NO.
FROM "PERMIT TO DRILL WELL"

110-94-1319

OWNER THURSH BRIAN
STREET OR RFD MINOR ROAD A.D. SHARP RD TOWN ECUMER
SUBDIVISION SHARP FARM SECTION 1 LOT 34

WELL LOG

Not required for driven wells

GROUTING RECORD

WELL HAS BEEN GROUTED
(Circle Appropriate Box)YES NO
☒ Y ☐ N

TYPE OF GROUTING MATERIAL (Circle one)

CEMENT ☒ CM BENTONITE CLAY ☐ BCNO. OF BAGS 18 NO. OF POUNDS 1800GALLONS OF WATER 110

DEPTH OF GROUT SEAL (to nearest foot)

from 0 ft. to 60 ft.
(enter 0 if from surface)CASING RECORD
casing types insert appropriate code below
☒ ST STEEL ☐ CO CONCRETE
☐ PL PLASTIC ☐ OT OTHERMAIN CASING TYPE ST
Nominal diameter top (main) casing (nearest inch) 6
Total depth of main casing (nearest foot) 60OTHER CASING (if used)
diameter inch depth (feet) from to SCREEN RECORD
screen type or open hole
☒ ST STEEL ☐ BR BRASS ☐ HO OPEN
☐ PL PLASTIC ☐ OT OTHERSTATE THE KIND OF FORMATIONS PENETRATED, THEIR
COLOR, DEPTH, THICKNESS AND IF WATER BEARING

DESCRIPTION (Use additional sheets if needed)	FEET		check if water bearing
	FROM	TO	
Topsoil	0		
Sandy clay	1	3	
Yellow Sand	3	14	
Sandy clay	14	22	
Sandy Br. Mica	22	38	
Tan Sandy Mica	38	46	
Sandy Br. Mica w/quartz	46	53	✓
Grav. Br.	53	60	
Fractured Granite	60	65	✓
Granite	65	73	
Br Sandstone	73	75	✓
Granite	75	160	

NUMBER OF UNSUCCESSFUL WELLS: 0WELL HYDROFRACTURED ☐ YES ☒ NOCIRCLE APPROPRIATE LETTER
A A WELL WAS ABANDONED AND SEALED WHEN THIS WELL WAS COMPLETED
E ELECTRIC LOG OBTAINED
P TEST WELL CONVERTED TO PRODUCTION WELLI HEREBY CERTIFY THAT THIS WELL HAS BEEN CONSTRUCTED IN
ACCORDANCE WITH COMAR 26.04.04 "WELL CONSTRUCTION" AND
IN CONFORMANCE WITH ALL CONDITIONS STATED IN THE ABOVE
CAPTIONED PERMIT, AND THAT THE INFORMATION PRESENTED
HEREIN IS ACCURATE AND COMPLETE, TO THE BEST OF MY
KNOWLEDGE.DRILLERS LIC. NO. MWD 040
Bevise F. Easterday
DRILLERS SIGNATURE
(MUST MATCH SIGNATURE ON APPLICATION)LIC. NO. MWD 386
Wendy Blangsted
SITE SUPERVISOR (sign of driller or journeyman
responsible for sitework if different from permittee)GRAVEL PACK
IF WELL DRILLED,
WAS FLOWING WELL
INSERT F IN BOX 68 MDE USE ONLY
(NOT TO BE FILLED IN BY DRILLER)
T (E.R.O.S.) W Q
70 72 74 75 76
TELESCOPE LOG OTHER DATA
CASING INDICATOR

C3

PUMPING TEST

HOURS PUMPED (nearest hour) 3PUMPING RATE (gal. per min.) 12METHOD USED TO MEASURE PUMPING RATE Bucket

WATER LEVEL (distance from land surface)

BEFORE PUMPING 23 ft.WHEN PUMPING 38 ft.

TYPE OF PUMP USED (for test)

☒ A air ☐ P piston ☐ T turbine
☐ C centrifugal ☐ R rotary ☐ O other (describe below)
☐ J jet ☒ S submersible

PUMP INSTALLED

DRILLER WILL INSTALL PUMP YES ☒ NO ☐IF DRILLER INSTALLS PUMP, THIS SECTION
MUST BE COMPLETED FOR ALL WELLS.TYPE OF PUMP INSTALLED
PLACE (A,C,J,P,R,S,T,O)
IN BOX 29 CAPACITY:
GALLONS PER MINUTE
(to nearest gallon) 31 35PUMP HORSE POWER 37 41PUMP COLUMN LENGTH
(nearest ft.) 43 47CASING HEIGHT (circle appropriate box
and enter casing height)☒ + above 49
☐ - below 2 (nearest foot)

LOCATION OF WELL ON LOT

SHOW PERMANENT STRUCTURE SUCH AS
BUILDING, SEPTIC TANKS, AND /OR
LANDMARKS AND INDICATE NOT LESS
THAN TWO DISTANCES.
(MEASUREMENTS TO WELL)Keen Hope10'10'10'10'10'10'10'10'10'10'

COUNTY

Review OK Km 12/16/97

FIELD DATA SHEET
HOWARD COUNTY WELL YIELD TEST

Well Permit No. HO - 94-1319

Location of property (road) TRINDELPHIA RD / SHARP RD.

Subdivision SHARP FARM

Well Driller EASTEN DAY

Lot

Block

Plat

² Sec

Owner

THRU 5/1

Depth of well 160 20 GPM

Distance of measuring point (M.P.) above ground 2'

Static water level (S.W.L.) below M.P. 23'

I. High rate pumping -- reservoir drawdown

Time pump started 1:15



Pumping rate

12 GPR

Total time 17.5 to reach pumping water level 12 ft. below M.P.

II. Recovery pump test data - observations to be recorded every 15 minutes

[illegible]

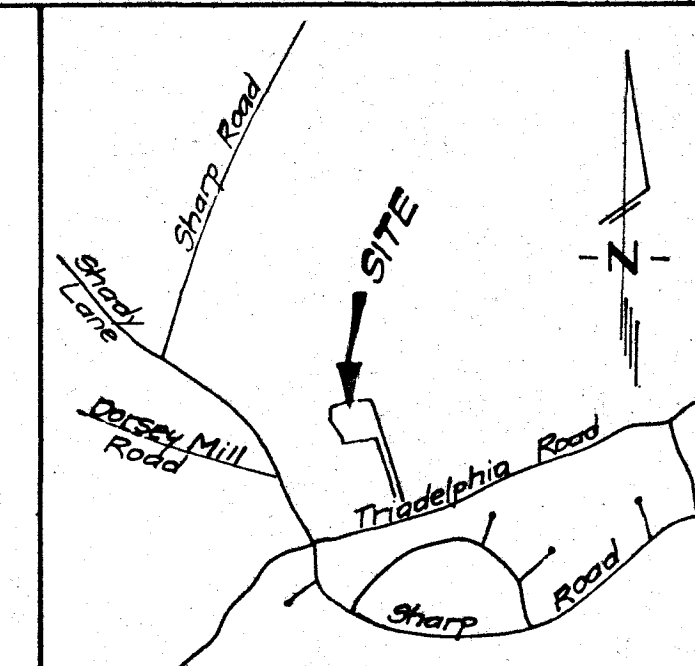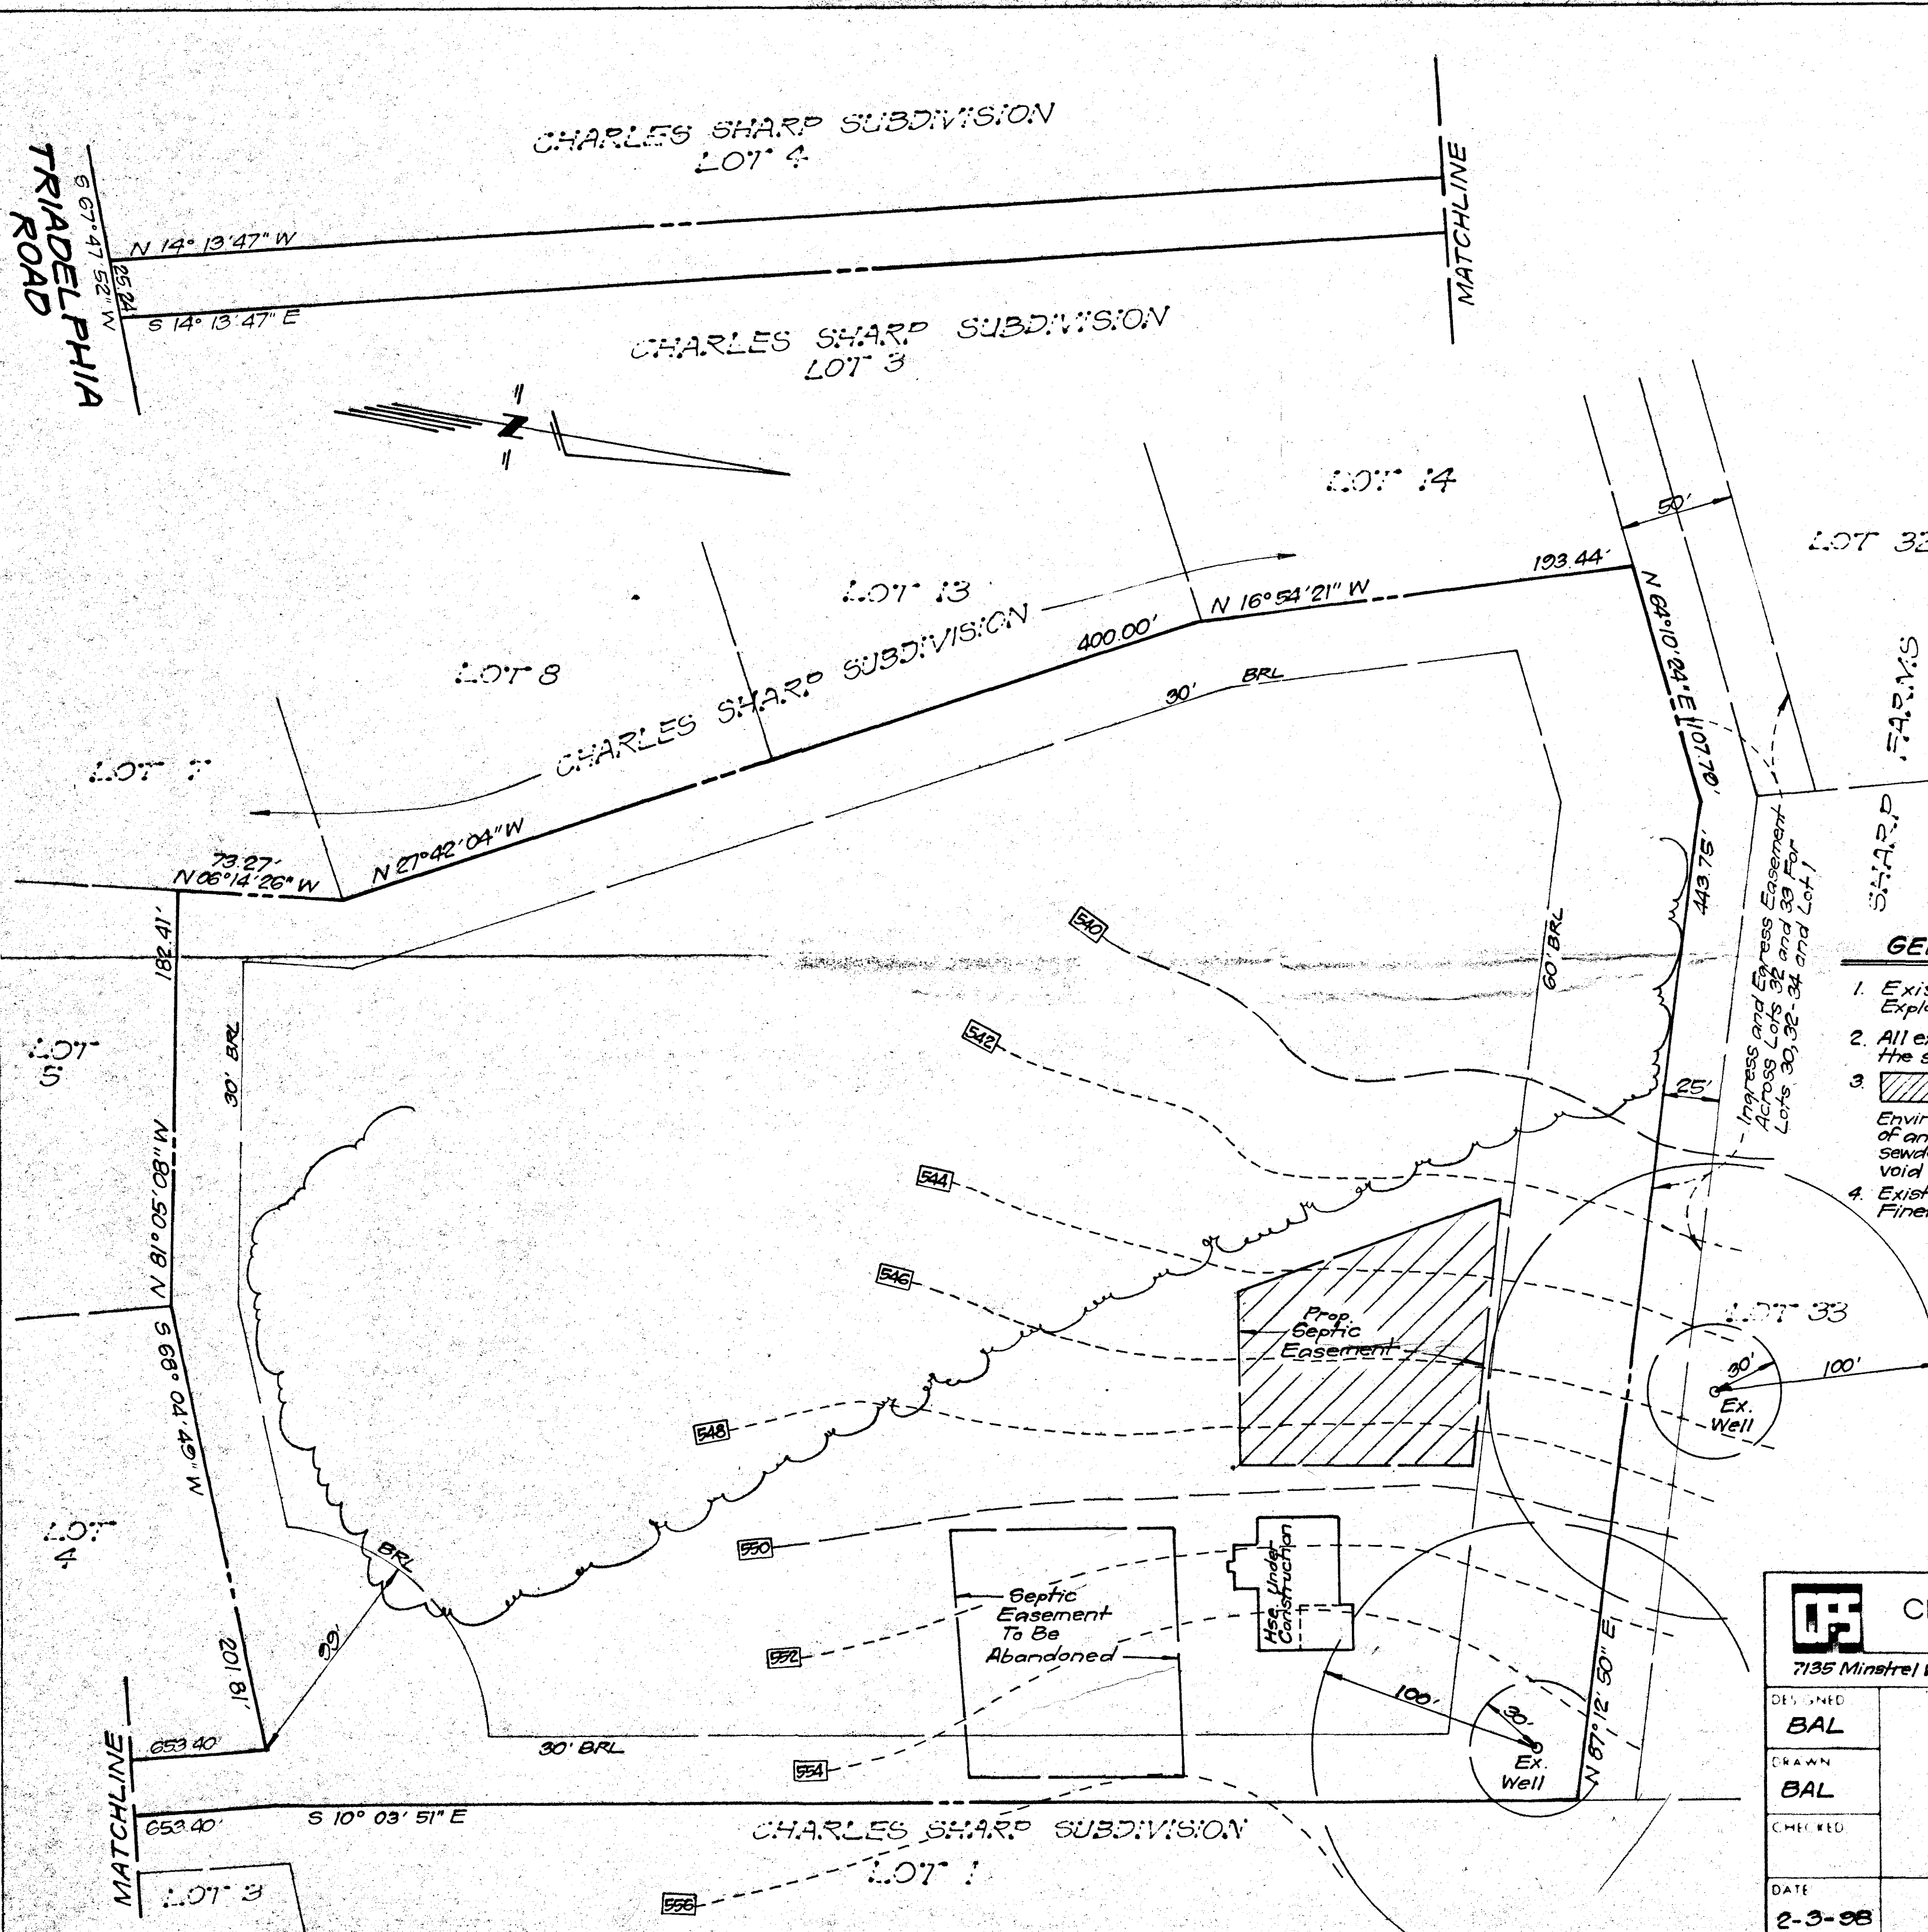

VICINITY MAP
Scale: 1" = 2000'

LEGEND

Contour Interval	2 Ft.
Existing Contour	540
Passed Percolation Test	
Fit w/ Spot Elevation	

- GENERAL NOTES**
- Existing topography was taken from plans prepared by Exploration Research, Inc.
 - All existing wells and septic systems within 100' feet of the subject property have been shown.
 - This area is a private sewerage easement of 10,000 sq. ft. as required by The Md. State Dept. of the Environment for individual sewage disposal. Improvements of any nature in this area are restricted until public sewage is available. This easement shall become null and void upon connection to public sewage.
 - Existing percolation test holes were field located by Clark-Finefrock and Sackett, Inc. on

APPROVED: For Onsite private water and sewerage systems. Howard County Health Dept.

County Health Officer _____ Date _____

CLARK • FINEFROCK & SACKETT, INC. ENGINEERS • PLANNERS • SURVEYORS 7135 Minstrel Way • Columbia, Md. 21045 • (410) 381-7500 Balt. • (301) 621-8100 Wash.		
DESIGNED BAL	PERC CERTIFICATION PLAT 3051 SHARP ROAD LOT 34 SHARP FARMS FOURTH ELECTION DISTRICT HOWARD COUNTY, MARYLAND For: BRIAN THRUSH 11616 Clock Tower Lane Laurel, Md. 20708	SCALE As Shown
DRAWN BAL		DRAWING 1 OF 1
CHECKED		JOB NO. 97-187
DATE 2-3-98		FILE NO. 97-187X



HOWARD COUNTY HEALTH DEPARTMENT

Joyce M. Boyd, M.D., County Health Officer
January 7, 1998

MEMORANDUM

TO: Bryan and Lisa Thrush
11616 Clocktower Lane
Laurel, MD 20708

FROM: Craig Williams, Program Director (CW)
Water and Sewerage Program
Bureau of Environmental Health

RE: Building Permit Serial Number: B00109312
Lot ID: Sharp Farms Lot 34
3951 Sharp Road, Glenwood, Maryland 21738

This office has received your Building Permit Application Serial Number B00109312, but is unable to recommend approval because of the impact to the established sewage disposal easement.

- To maintain the house in the proposed location, successful Percolation Testing would be needed to support the requisite change in septic location. To initiate this process, please complete the attached percolation Test Application and return it to this office with a copy of the site plan and the \$225 test fee. Then a test date can be scheduled.
- The alternative would be to submit a revised site plan for a house location that maintains the required separation from the recorded sewage easement. Such a revision should be submitted through the Building Permit Office since the altered house location would require review by several agencies.

If you have any questions please call 410-313-2640.

CW:tl

cc: Department of Licenses and Permits
D.W. Taylor Associates, Inc.
Clark Finefrock & Sackett - Joey Ecker
File ✓

UPON RECONSIDERATION/
MODIFICATION
ACCEPTED AS
PROPOSED.
1/26/98
CW
