

9/11/78
1:00 p.m.

app 9.18.78
D

P 28625

PERMIT

SEWAGE DISPOSAL SYSTEM

A REPAIR

MARYLAND STATE DEPARTMENT OF HEALTH*

HOWARD COUNTY

ELLICOTT CITY

DISTRICT _____

INDEXED

DATE 8/2/78

Bud Arnold IS PERMITTED TO INSTALL _____ ALTER X

ADDRESS _____ PHONE _____

SUBDIVISION _____ ROAD 1310 Route 94, Lisbon LOT _____

PROPERTY OWNER Raymond F. Mills little brown house next to Lisbon Fire House

ADDRESS 1310 Route 94, Lisbon, Md.

SPECIFICATIONS 2 bedrooms

SEPTIC TANK CAPACITY 1000 GALLONS

DRAIN FIELD _____ DEPTH _____ FEET, BOTTOM AREA _____ SQ. FT.

DEEP TRENCH _____ DEPTH _____ FEET, BOTTOM AREA _____ SQ. FT.

SEEPAGE PITS _____ ABSORBENT SIDE-WALL AREA _____ SQ. FT.

INLET PIPE _____ FT. BELOW ORIGINAL GRADE. MAXIMUM DEPTH _____ FT. BELOW ORIGINAL GRADE

EFFECTIVE DEPTH AT _____ FT. BELOW ORIGINAL GRADE.

LOCATE DISPOSAL AREA _____ FT. FROM _____ LOT LINE AND _____ FT. FROM _____ LOT LINE AS SEEN WHEN

FACING LOT FROM _____

WELL WATER ISSUE
RECTIFIED?

REPAIR- CALL FOR INSPECTION WHEN GROUND IS OPENED UP SO SANITARIAN CAN RECOMMEND

REPAIR. - Tile Fields - 3ft wide 3 1/2 ft deep - 1 1/2 stone under
Pipe - 100 running ft. of trench.

PLANS APPROVED BY Palmer F. Wine DATE 8/2/78

COVER NO WORK UNTIL INSPECTED AND APPROVED.

NEITHER THE HOWARD COUNTY COUNCIL NOR THE HEALTH DEPARTMENT IS RESPONSIBLE FOR THE SUCCESSFUL OPERATION OF ANY SYSTEM.

NOTE: IF TRENCH IS USED CALL FOR INSPECTION BEFORE PLACING GRAVEL IN TRENCH.

NOTE: NO DRY WELL SHALL EXCEED 15 FOOT IN DIAMETER.

NOTE: ALL PIPE FROM HOUSE TO DISPOSAL AREA MUST BE CAST IRON.


PERMIT VOID AFTER THREE YEARS.

NOTE: INSTALL STAND PIPE ON SEPTIC TANK AND DRY WELL. STAND PIPES MUST BE 6 INCHES IN DIAMETER. CAST IRON, CONCRETE OR TERRA COTTA ACCEPTED.

*INSTALLER IS RESPONSIBLE FOR OBTAINING FINAL APPROVAL ON THIS PERMIT.

P 28625

28
35
29
36
115

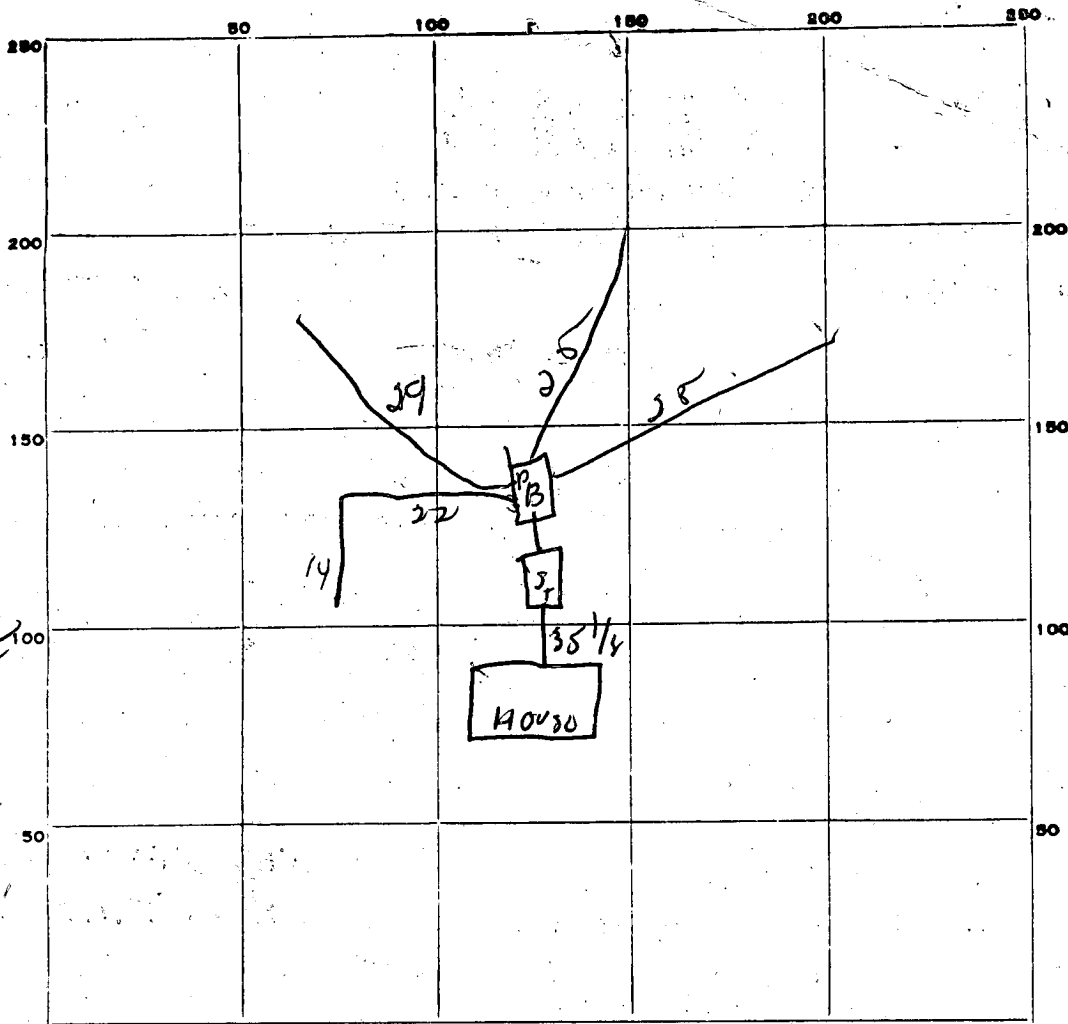

INDICATE NORTH. - NAME ADJOINING ROADWAY AS BASE LINE.

PERMIT CARD OK NIP

SEPTIC TANK, LEVEL 012

CLEANOUTS OK

DISTRIBUTION BOX, LEVEL OK

TILE FIELD, DEPTH 4 FT. TRENCH WIDTH 3 FT.

GRAVEL DEPTH 18 IN. TOTAL LENGTH 115 FT.

NUMBER OF TRENCHES 4 TOTAL BOTTOM AREA 345

SEEPAGE PITS, INSIDE DIAMETER _____ FT. DEPTH BELOW INLET _____ FT.

ABSORBENT AREA _____ SQ. FT.

REMARKS _____

DATE SYSTEM APPROVED 9/18/78

INSPECTOR Dev Monaghan

Call Mrs. Ferrara in order to gain access into house

FILE Well & Septic Inspection DATE REPORTED 6/29/78

PROPERTY OWNER Raymond Mills

P.O. ADDRESS 1310 Route 94

TELEPHONE _____

DIRECTIONS TO PROPERTY Lisbon, Md.

INFORMANT Martha Ferrara 465-6400 - home - 465-0809

Temple Real Est.

4296 Montgomery Rd.

Ellicott City, Md. 21043

CONDITION FOUND Be.t. P 769 10:40 Am 7/5/78 (PS)

Dry well full. Level is up in stand pipe ~~at~~ less than 2 feet below ground. Has been almost to top. Had 2 days of rain July 2nd and 3rd.

hold for water sample

Letter 7-6-78 Needs septic Repair (PS)

ACTION TAKEN

H-1, B-2 letter 7/13/78 (PS)

Mrs Mills 489-4233

FINAL DISPOSITION _____

July 6, 1978

Martha Ferrara
Grempler Realty
4296 Montgomery Road
Ellicott City, Md. 21043

Dear Ms. Ferrara:

At your request, I inspected the sewage disposal system at 1310 Route 94, Lisbon, Md. on July 5, 1978. My inspection revealed that the dry well was filled to capacity. This condition indicates that the soil around the dry well is no longer absorbing the sewage as efficiently as it should and the sewage disposal system is failing.

To correct this problem, you or your buyer must apply to this office for a permit and percolation test for a repair system.

Very truly yours,

Lawrence Spilker

LS:ds

July 17, 1978

Ms. Martha Ferrara
Grempler Real Estate
4296 Montgomery Road
Ellicott City, Md. 21043

RE: 1310 Route 94
Raymond Mills

Dear Ms. Ferrara:

The tests run on the above referenced water supply shows the presence of bacteria that may be harmful to your health.

In order to correct this, you should have the well checked for breaks in the lines or seals or other structural defects. Then, you should have the well disinfected as shown in the enclosed literature.



When you have done this, call the Health Department and we will be glad to arrange for further testing.

Very truly yours,

Lawrence J. Spilker

LJS:ds

Enclosure

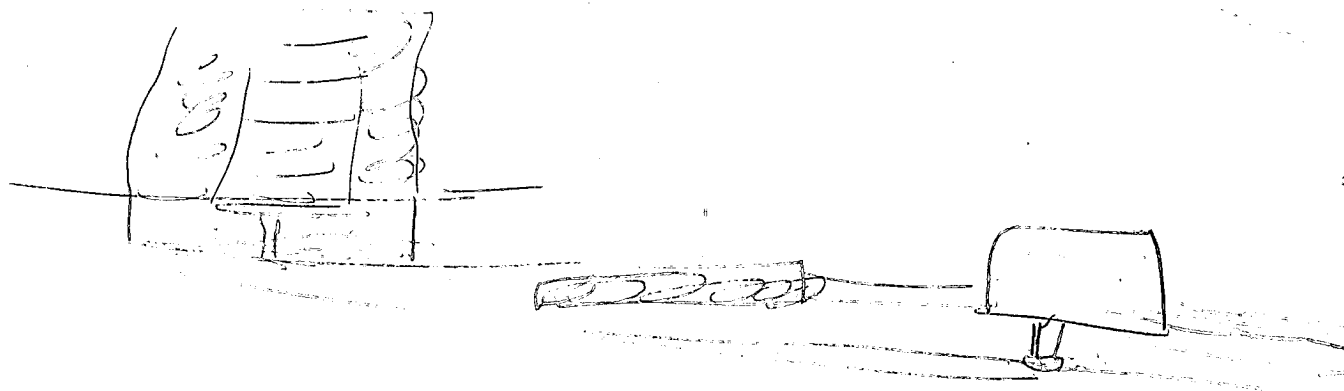

h, b x

150
