

4-28-77 if possible, if not 4-27-77 partial W2

PERMIT

SEWAGE DISPOSAL SYSTEM

MARYLAND STATE DEPARTMENT OF HEALTH
HOWARD COUNTY

25614

18841

ELLICOTT CITY

DISTRICT 3rd

DATE 4/11/77

INDEXED

Albert Schoel

IS PERMITTED TO INSTALL ☒ ALTER

ADDRESS 3620 School Drive, Ellicott City, Md. 21043

PHONE 531-6677

A SEWAGE DISPOSAL SYSTEM LOCATED AT

SUBDIVISION Wayside Estates

3604 School Drive
ROAD Wayside Drive

LOT 7, Blk. B, Sec. 1

PROPERTY OWNER Albert Schoel

Dave & Robin Murray

ADDRESS same as above

SPECIFICATIONS 3 bedrooms

DRAIN FIELD DEPTH FEET, BOTTOM AREA SQ. FT.

SEEPAGE PITS ABSORBENT SIDE-WALL AREA SQ. FT.

SEPTIC TANK CAPACITY 1000 GALLONS

FOR GARBAGE GRINDER, INCREASE DISPOSAL AREA 22% & TANK CAPACITY 50%.

OTHER DRY WELL AND TRENCH - The dry well will be located 25 ft. from the front property line and 85 ft. in from the right property line. The invert will be 3 ft. below original grade with a maximum depth of 10 ft. below original grade. The dry well will be 15' x 15' square and 10 ft. deep for a total sidewall area of 420 sq. ft. The trench will begin 5 ft. from the edge of the dry well and follow the contour of the land. The trench will be 2 ft. wide, 10 ft. deep, 25 ft. long, and have 7 ft. of stone. Lot line determined as you face from the road. NOTE: CALL FOR INSPECTION BEFORE PLACING STONE IN TRENCH. NOTE: ALL PIPE FROM HOUSE TO DISPOSAL AREA MUST BE CAST IRON. PERMIT VOID AFTER THREE YEARS. NOTE: INSTALL STAND PIPE ON SEPTIC TANK AND DRY WELL. STAND PIPES MUST BE 6 INCHES IN DIAMETER. CAST IRON, CONCRETE OR

PLANS APPROVED BY Robert T. Moorefield
TERRA COTTA ACCEPTED.

DATE 1/3/76

FILL SEPTIC TANK AND DISTRIBUTION BOX WITH WATER BEFORE CALLING FOR AN INSPECTION. COVER NO WORK UNTIL INSPECTED AND APPROVED.


NEITHER THE HOWARD COUNTY COMMISSIONERS NOR THE HEALTH DEPARTMENT IS RESPONSIBLE FOR THE SUCCESSFUL OPERATION OF ANY SYSTEM.

BUDG. PERMIT SIGNED
AND RETURNED

Serial # 30915
extended by extension, kiki

18841

DATE SYSTEM APPROVED

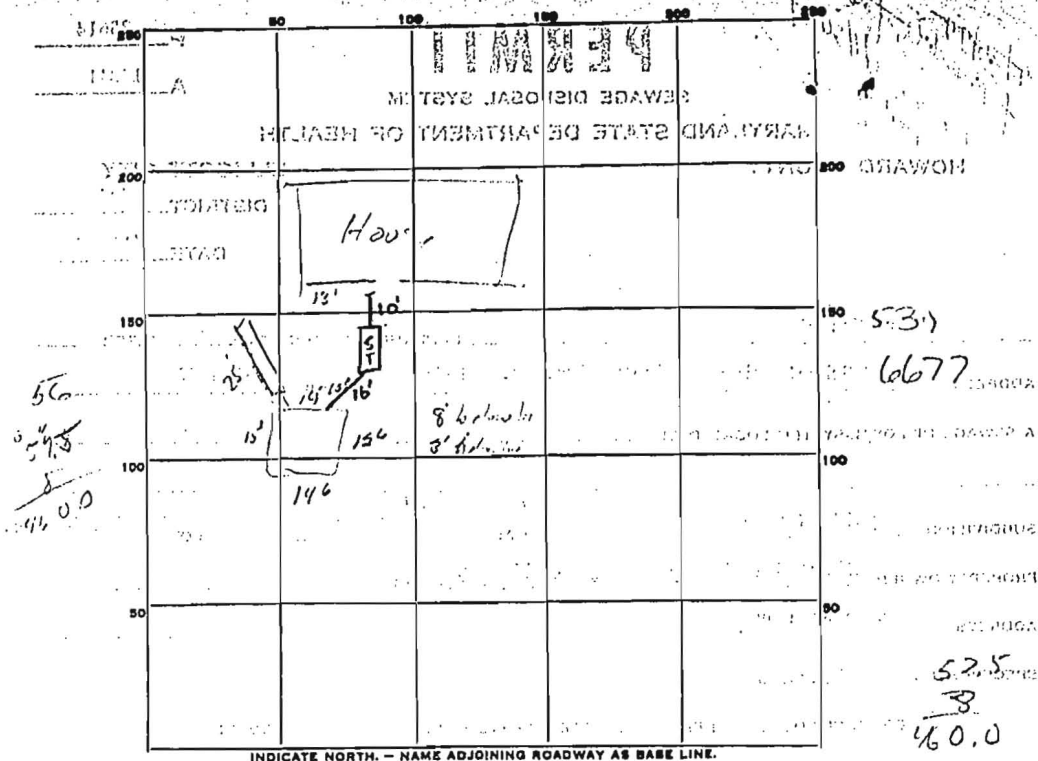

PERMIT CARD Partial Adm

SEPTIC TANK, LEVEL 1000 CLEANOUTS N.1 ✓ ✓

DISTRIBUTION BOX, LEVEL 11.4

TILE FIELD, DEPTH 11-12 FT. TRENCH WIDTH 2 FT.

GRAVEL DEPTH 7 1/2 FT (7' eff. depth) IN. TOTAL LENGTH 25 FT.

NUMBER OF TRENCHES 1 SIDEWALL TOTAL BOTTOM AREA 175 187

SEEPAGE PITS, INSIDE DIAMETER 57.5 FT. DEPTH BELOW INLET 8 FT. 7 eff

ABSORBENT AREA 402.5 SQ. FT. in DW; TOTAL 578

REMARKS Soaker to help stuff - influenced trench 1' to 2' deep

will OK this time but water cannot lid

DDW 5.30 OK ✓ Stone depth DDW

4/27/77 10:45 AM - No change - not ready til PM WWZ

4/27/77 3:30 PM - OK to cover all except house → ST conn. WWZ

OK'd by PFW 12/19/77

DATE SYSTEM APPROVED _____ INSPECTOR _____

PRELIMINARY

APPLICATION

18841

SEWAGE DISPOSAL TESTING

STATE OF MARYLAND - DEPARTMENT OF HEALTH AND MENTAL HYGIENE

HOWARD COUNTY HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH SERVICES

P. O. BOX 476, ELLICOTT CITY, MARYLAND 21043
TELEPHONE: 469-8000, EXT. 396

DISTRICT 3rd

DATE 8/3/73

TO: THE COUNTY HEALTH OFFICER
ELLICOTT CITY, MARYLAND

I, HEREBY, APPLY FOR THE NECESSARY TEST IN ORDER TO CONSTRUCT (OR RECONSTRUCT) A SEWAGE DISPOSAL SYSTEM.

PROPERTY OWNER G. Albert Scheel, Jr.

ADDRESS 12845 Philadelphia Road, Ellicott City, Md. PHONE Boender - 465-7777

PROPERTY LOCATION:

SUBDIVISION Wayside Estates LOT NO. 7, Blk. B, Sect. 1

ROAD AND DESCRIPTION Wayside Drive

SIZE OF LOT 1 acre TYPE BLDG. 3 or 4 bedrooms

NUMBER OF BEDROOMS

IF NOT SINGLE RESIDENCE DESCRIBE

THE SYSTEM INSTALLED UNDER THIS APPLICATION IS ACCEPTABLE ONLY UNTIL PUBLIC FACILITIES BECOME AVAILABLE.

SIGNATURE OF APPLICANT /s/ G. Albert Scheel, Jr.

APPROVED BY FOR DATE

(KIND OF SYSTEM)

REJECTED BY FOR DATE

(KIND OF SYSTEM)

HOLD PENDING FURTHER TESTS DATE

REASONS FOR REJECTION OR HOLDING

THIS IS NOT A PERMIT

PAUL LEE

Lot. 7B

INDICATE NORTH - NAME ADJOINING ROADWAY AS BASE LINE.
Wynode Dr. to Trindelfheim →

Antib'

Ar-true
- 9 mms
Max
Depth

TYPE OF SOIL

TYPE OF SOIL *Mud*

STATE OF MARYLAND
WATER RESOURCES ADMINISTRATION
TAWES STATE OFFICE BLDG., ANNAPOLIS, MD. 21401
WELL COMPLETION REPORT

THIS REPORT MUST BE SUBMITTED WITHIN 30 DAYS AFTER WELL COMPLETION.
 FILL IN THIS FORM COMPLETELY

C 1 7810 (SEQ. NO.) 6
 (THIS NUMBER IS TO BE PUNCHED IN COLUMNS 2-6 ON ALL CARDS)

DATE RECEIVED (MRA USE ONLY) 10-24-76
 DATE WELL COMPLETED 11-1-76
 DEPTH OF WELL 200 (TO NEAREST FOOT)

PERMIT NO. FROM "PERMIT TO DRILL WELL" 11-1-76-1117
 COUNTY NUMBER 42
 DRILLER'S IDENTIFICATION NO. 42

OWNER: Robert Albert
 LAST NAME FIRST NAME
 STREET OR RFD: Talbot Station Rd. POST OFFICE: Talbot Station, Md.

WELL LOG
 STATE THE KIND OF FORMATIONS PENETRATED, THEIR COLOR, DEPTH, THICKNESS AND IF WATER BEARING

DESCRIPTION (USE ADDITIONAL SHEETS IF NECESSARY)	FEET		CHECK IF WATER BEARING
	FROM	TO	
Topsoil	0	2	
Gravelly Sand	2	100	
Mud	100	200	

GROUTING RECORD
 WELL HAS BEEN GROUTED (CIRCLE APPROPRIATE BOX) YES ☒ NO ☐
 TYPE OF GROUTING MATERIAL (CIRCLE BOX) CEMENT ☒ BENTONITE CLAY ☐
 NO. OF BAGS 20 NO. OF POUNDS 2000
 GALLONS OF WATER 140
 DEPTH OF GROUT SEAL (TO NEAREST FOOT) FROM 0 FT. TO 28 FT.
 (ENTER 0 IF FROM SURFACE)

CASING RECORD
 Casing Types: INSERT APPROPRIATE CODE BELOW
 STEEL ☒ CONCRETE ☐
 PLASTIC ☐ OTHER ☐
 MAIN CASING TYPE: OT
 NOMINAL DIAMETER TOP (MAIN) CASING (NEAREST INCH) 6
 TOTAL DEPTH OF MAIN CASING (NEAREST FOOT) 80

OTHER CASING (IF USED)
 DIAMETER (INCH) DEPTH (FEET) FROM TO

SCREEN RECORD
 SCREEN TYPE OR OPEN HOLE: INSERT APPROPRIATE CODE BELOW
 STEEL ☒ BRASS OR BRONZE ☐ OPEN HOLE ☐
 PLASTIC ☐ OTHER ☐

PUMPING TEST
 HOURS PUMPED (TO NEAREST HOUR) 2
 PUMPING RATE (GALLONS PER MINUTE TO NEAREST GALLON) 1
 METHOD USED TO MEASURE PUMPING RATE: Pumped
 WATER LEVEL (DISTANCE FROM LAND SURFACE) BEFORE PUMPING 50 (NEAREST FOOT)
 WHEN PUMPING 22 (NEAREST FOOT)
 TYPE OF PUMPED USED (CIRCLE APPROPRIATE BOX) (FOR PUMPING TEST)
 AIR ☐ PISTON ☐ TURBINE ☐
 CENTRIFUGAL ☐ ROTARY ☐ OTHER (DESCRIBE BELOW)
 JET ☐ SUBMERSIBLE ☐

PUMP INSTALLED
 TYPE OF PUMP (WRITE APPROPRIATE LETTER IN BOX - SEE ABOVE: A, C, J, P, R, S, T, O)
 DRILLER WILL INSTALL PUMP (CIRCLE APPROPRIATE BOX) YES ☐ NO ☒
 CAPACITY: GALLONS PER MINUTE (TO NEAREST GALLON) 31 30
 PUMP HORSE POWER 37 41
 PUMP COLUMN LENGTH (NEAREST FOOT) 43 47


CASING HEIGHT (CIRCLE APPROPRIATE BOX AND ENTER CASING HEIGHT)
 ABOVE ☐ BELOW ☒ LAND SURFACE 7 (NEAREST FOOT)

LOCATION OF WELL ON LOT
 SHOW PERMANENT STRUCTURE SUCH AS BUILDINGS, SEPTIC TANKS, AND/OR OTHER LAND MARKS AND INDICATE NOT LESS THAN TWO DISTANCES (MEASUREMENTS TO WELL).

CIRCLE APPROPRIATE BOXES
 A WELL WAS ABANDONED AND SEALED WHEN THIS WELL WAS COMPLETED
 E ELECTRIC LOG OBTAINED
 P TEST WELL CONVERTED TO PRODUCTION WELL
 I HEREBY CERTIFY THAT I HAVE COMPLIED WITH ALL CONDITIONS STATED ON THE ABOVE-CAPTIONED "PERMIT TO DRILL WELL", AND THAT INFORMATION CONTAINED IN THIS REPORT IS TRUE, ACCURATE, AND COMPLETE TO THE BEST OF MY KNOWLEDGE, INFORMATION AND BELIEF.

DRILLER'S NAME: J. P. Smith
 (PLEASE PRINT)
 SIGNATURE: J. P. Smith

DIAMETER OF SCREEN 36 (NEAREST INCH) FROM 36 TO 60
 GRAVEL PACK
 IF WELL DRILLED WAS A FLOWING WELL CIRCLE BOX 68 ☐
 WRA USE ONLY (NOT TO BE FILLED IN BY DRILLER) (E.R.O.S.)
 YES ☐ NO ☐
 TELESCOPE CASING LOG INDICATOR 74 75 76 OTHER DATA AVAILABLE

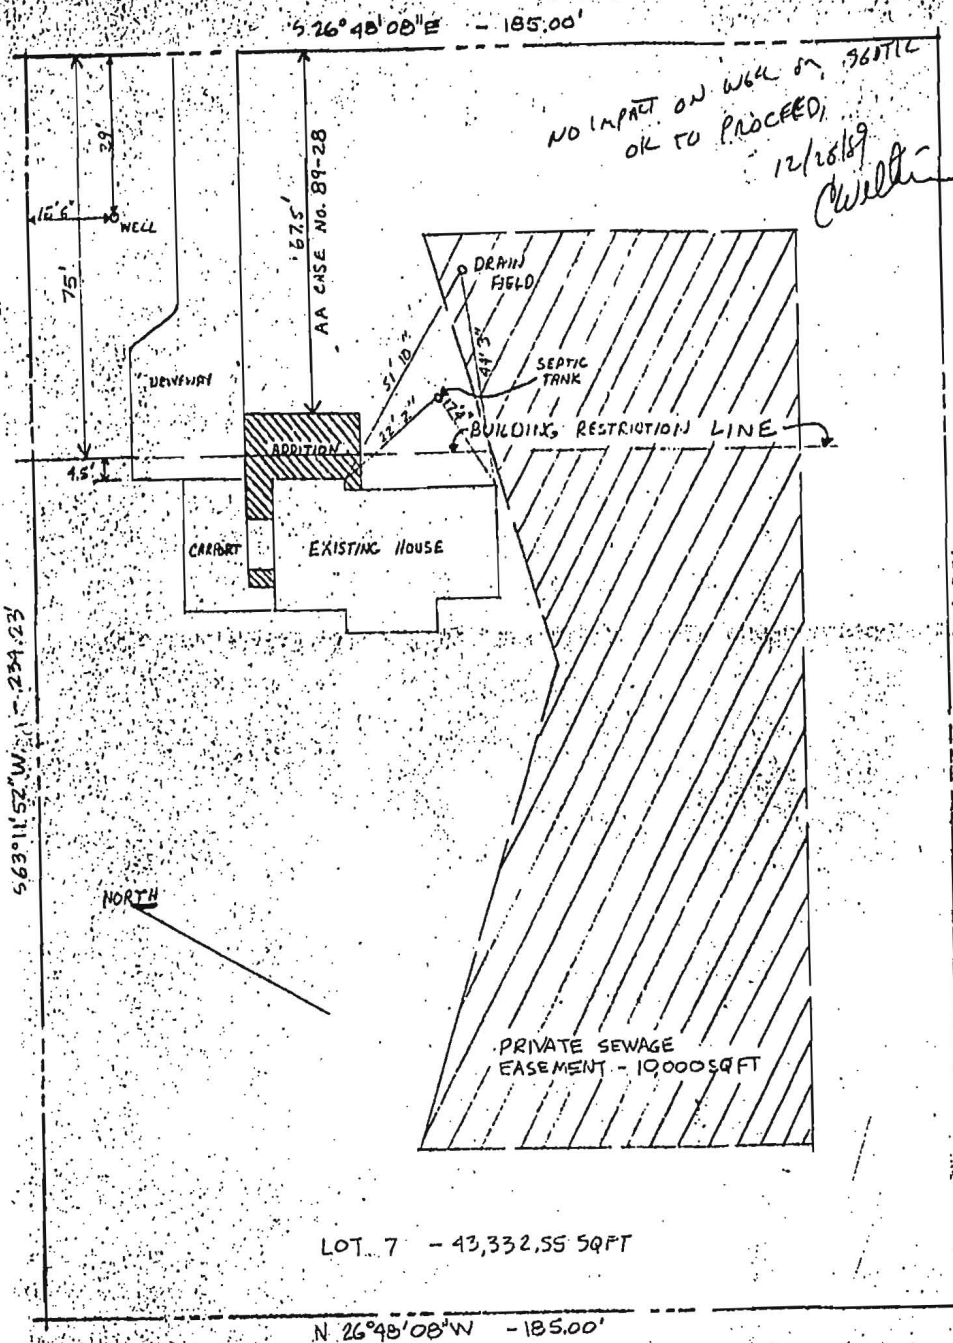

SITE PLAN
SCALE 1" = 20'

3604

P. 25614 A 18841
DATE 4/11/77

LOCATION	<u>Wayside Estates</u>	APPLICATION	
	<u>School Drive</u>	HOLD	()
		APPROVED	(✓)
		REJECTED	()
LOT	<u>7, Blk B, Sec. 1</u>		
APPLICANT	<u>1st St. Albert School</u>	INSTALLATION	
OWNER	<u>Albert School</u>	HOLD	()
	<u>DAVID MURPHY</u>	APPROVED	(✓)
PERMITTEE	<u>Albert School</u>	APPROVED	<u>12/19/77</u>
		DATE	

HD - 11

re: Lastday's Wells
grouted illegally 10-12-76.

Report on Well Groutings of 10/11/76 Mon.

I arrived at Wayside Estates
Lot 7 on School Drive at about
100 P.M. and waited for
the Well Grout Truck to
arrive. The well grout truck
arrived at about 130 & started
grouting the well. The well
had 80 ft of casing & at
least 58 ft depth to be grouted.
The grout machinery worked
slower than usual and as a
result the well grout was
not finished till 4.15 P.M.

28 bags of cement were used.
There were two other well grouts
on the schedule Calm Hill Lot 11
and Wayside Estates Lot 3
but ~~so~~ we did not have time to
~~complete~~ grout these wells. I said
we could not observe well grouts on 10/12/76 Holiday
Raymond Hodger

P.S. Well on Lot 7 is approved now
I think we could have grouted both wells
in Wayside Estates if well grout pumps were working good
but I do not think we could ^{have} grouted all 3 wells
on schedule of 10/11/76

re: Eastside's well
grouted illegally 10-12-76

Report on Wall Groutings of 10-11-76 MON.

I arrived at Wayside Estates lot 7 on Scheel Dr. at about 100 P.M. and waited for the well grout truck to arrive. The well grout truck arrived at about 130 & started grouting the well. The well had 80 ft. of casing & at least 58 ft. to be grouted. The grout machinery worked slower than usual and as a result the well grout was not finished till 4:15 P.M. 28 bags of cement were used. There were two other well grouts on the schedule Cabin Hill lot 11 and Wayside Estates lot 3 but we did not have time to grout these wells. I said we could not observe well grouts on 10-12-76 Holiday
Raymond Hodges

P.S. Well on lot 7 is approved now. I think we could have grouted both wells in Wayside Estates if well grout pumps were working good but I do not think we could have grouted all 3 wells on schedule of 10-11-76.

Report on Well Groutings of 10/11/76 Mon.

I arrived at Wayside Estates
Lot 7 on Scheel Drive at about
1:00 P.M. and waited for
the Well Grout Truck to
arrive. The well grout truck
arrived at about 1:30 & started
grouting the well. The well
had 80 ft of casing & at
least 58 ft depth to be grouted.
The grout machinery worked
slower than usual and as a
result the well grout was
not finished till 4:15 P.M.

28 bags of cement were used.
There were two other well grouts
on the schedule Calm Hill Lot 11
and Wayside Estates Lot 3
but ~~so~~ we did not have time to
~~complete~~ grout these wells. I said
we could not observe well grouts on 10/12/76 Holiday
Raymond Hodges

P.S. Well on Lot 7 is approved now.
I think we could have grouted both wells
in Wayside Estates if well grout pumps were working good
but I do not think we could ^{have} grouted all 3 wells
on schedule of 10/11/76

Report on Well Groutings
of 10-11-76 MON.

I arrived at Wayside Estates lot 7 on Scheel Dr. at about 1:00 P.M. and waited for the well grout truck to arrive. The well grout truck arrived at about 1:30 & started grouting the well. The well had 80 ft. of casing & at least 58 ft. to be grouted. The grout machinery worked slower than usual and as a result the well grout was not finished till 4:15 P.M. 28 bags of cement were used. There were two other well grouts on the schedule Cabin Hill lot 11 and Wayside Estates lot 3 but we did not have time to grout these wells. I said we could not observe well grouts on 10-12-76 Holiday
Raymond Hodges

P.S. Well on lot 7 is approved now. I think we could have grouted both wells in Wayside Estates if well grout pumps were working good but I do not think we could have grouted all 3 wells on schedule of 10-11-76.

printed 10-12-76

Report on Well Groutings of 10/11/76 Mon.

I arrived at Wayside Estates
Lot 7 on School Drive at about
100 P.M. and waited for
the Well Grout Truck to
arrive. The well grout truck
arrived at about 130 & started
grouting the well. The well
had 80 ft of casing & at
least 58 ft depth to be grouted.
The grout machinery worked
slower than usual and as a
result the well grout was
not finished till 4.15 P.M.

28 bags of cement were used.
There were two other well grouts
on the schedule Calm Hill Lot 11
and Wayside Estates Lot 3
but ~~so~~ we did not have time to
~~inspect~~ grout these wells. I said
we could not observe well grouts on 10/12/76 Holiday

Raymond Hodges

P.S. Well on Lot 7 is approved now.
I think we could have grouted both wells
in Wayside Estates if well grout pumps were working good.
But I do not think we could ^{have} grouted all 3 wells
on schedule of 10/11/76

Report on Well Groutings
of 10-11-76 MON.

I arrived at Wayside Estates lot 7 on Scheel Dr. at about 100 P.M. and waited for the well grout truck to arrive. The well grout truck arrived at about 130 & started grouting the well. The well had 80 ft. of casing & at least 58 ft. to be grouted. The grout machinery worked slower than usual and as a result the well grout was not finished till 4:15 P.M. 28 bags of cement were used. There were two other well grouts on the schedule Cabin Hill lot 11 and Wayside Estates lot 3 but we did not have time to grout these wells. I said we could not observe well grouts on 10-12-76 Holiday
Raymond Hodges

P.S. Well on lot 7 is approved now. I think we could have grouted both wells in Wayside Estates if well grout pumps were working good but I do not think we could have grouted all 3 wells on schedule of 10-11-76.

3
Xmas as no money we could grout all 3 wells

Report on Well Groutings of 10/11/76

I arrived at Wayside Estates
Lot 7 on School Drive at about
100 A.M. and waited for
the Well Grout Truck to
arrive. The well grout truck
arrived at about 130 & started
grouting the well. The well
had 80 ft of casing & at
least 58 ft depth to be grouted.
The grout machinery worked
slower than usual and as a
result the well grout was
not finished till 4.15 P.M.

28 bags of cement were used.
There were two other well grouts
on the schedule Calm Hill Lot 11
and Wayside Estates Lot 3
but ~~so~~ we did not have time to
~~inspect~~ grout these wells. I said
we could not observe well grouts on 10/12/76 Holiday
Raymond Hodges

P.S. Well on Lot 7 is approved now.
I think we could have grouted both wells
in Wayside Estates if well grout pumps were working good.
But I do not think we could ^{have} grouted all 3 wells
on schedule of 10/11/76
