

APPLICATION

A. 25885

SEWAGE DISPOSAL TESTING

STATE OF MARYLAND - DEPARTMENT OF HEALTH AND MENTAL HYGIENE

HOWARD COUNTY HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH SERVICES
P. O. BOX 476, ELLICOTT CITY, MARYLAND 21043
TELEPHONE: 465-5000, EXT. 356

DISTRICT 4
DATE 5/18/77

6/3/77
1:30 PM
DRY WELL 576 SFT SIDEWALL AREA
DRY WELL INLET TO BE ⁴12 FT DEEP & EFFECTIVE ^{AREA} TO START AT SA
DRY WELL. BOTTOM TO BE ¹²14 FT DEEP below original grade.
PLACE THE DRY WELL 75 FT FROM THE
OLD HOUSE & 60 FT FROM THE BACK LOT
LINE AS SEEN WHEN FACING THE
LOT FROM THE RIGHT OF WAY
TO THE COUNTY HEALTH OFFICER
ELLICOTT CITY, MARYLAND OK TO ADD DITCH OFF DW

I, HEREBY, APPLY FOR THE NECESSARY TEST IN ORDER TO CONSTRUCT (OR RECONSTRUCT) A SEWAGE
DISPOSAL SYSTEM. IF NECESSARY, STONE IN DITCH

PROPERTY OWNER LAURENCE W. STANTON ^{5 FT & 7 FT}
ADDRESS 1967 DAISY ROAD Woodbine, Md. PHONE 489-4739 ¹² ^{inspecting} ²⁷

PROPERTY LOCATION:

SUBDIVISION WARFIELDS Subdivision LOT NO. 3
ROAD AND DESCRIPTION About 1 1/2 miles so. of Rd 44 or 1967 Daisy Rd.
Left turn off of Daisy.

SIZE OF LOT 0.735 AC. TYPE BLDG. 3
NUMBER OF BEDROOMS

IF NOT SINGLE RESIDENCE DESCRIBE _____

THE SYSTEM INSTALLED UNDER THIS APPLICATION IS ACCEPTABLE ONLY UNTIL PUBLIC
FACILITIES BECOME AVAILABLE

SIGNATURE OF APPLICANT Laurence W. Stanton ^{Series No. 34356}
BLDG. PERMIT SIGNED
AND RETURNED 4/4/78


APPROVED BY Raymond Hodges FOR Drywell DATE 6/8/77
(KIND OF SYSTEM)

REJECTED BY _____ FOR _____ DATE _____
(KIND OF SYSTEM)

HOLD PENDING FURTHER TESTS _____ DATE _____

REASONS FOR REJECTION OR HOLDING 6/3/77 Held for review
with DM 6/6/77. No snout cannot be placed
at original place 6/8/77 Held for review
with DM LOT IS OK

THIS IS NOT A PERMIT

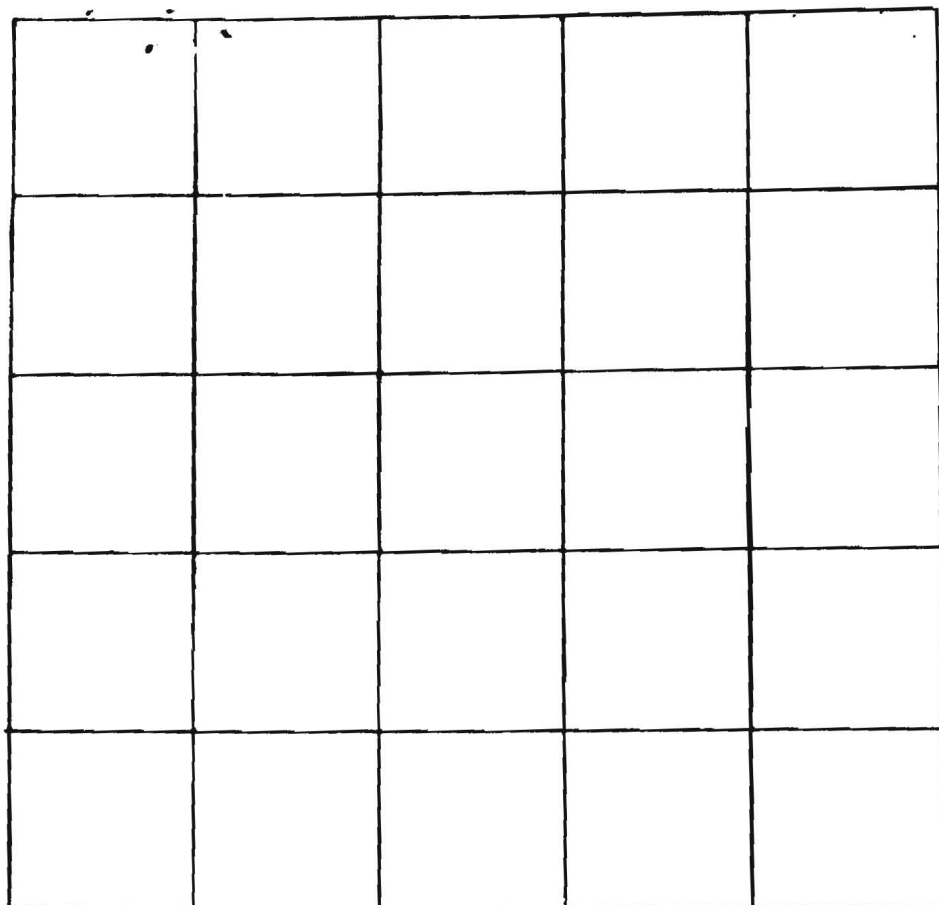

INDICATE NORTH - NAME ADJOINING ROADWAY AS BASE LINE

DATE	TEST NO.	DEPTH	PRE-WET		TEST - 1" DROP		TIME
			START	STOP	START	STOP	
6/3/77	1D	13 1/2	247	284	254	309	15
	1S	5 1/2	247	258	258	320	22
	2D	13	312	315	315	326	11
	2S	5	314	345	1st anch 31 min		30+
	3D	12	344	346	346	349	3
	3S	6	346	353	353	405	8
	2M	7	400	422	little pre Failed		30+
6/3/77	4	13	TOP BOT	4 FT 7 FT	7 C R A SANDY SILT L ODK		

REMARKS Existing House to Be torn Down & New House to be
 TYPE OF SOIL cracked. House built 15 yrs. We might have per
fect Records under name of DORSET OR WISE
 TESTED BY RAYMOND HOPKES ALSO PRESENT: JULIAN SMITH RELATIVE
H. S. R. K. BACKHOE
BEAN & STANTON
